
Priyanshu Upadhyay

Digital Transformation
&
Data Expert

Project Intelligence & Governance, Automation, Advance Work Package (AWP), Big Data Engineering, Dashboarding, and Analytics

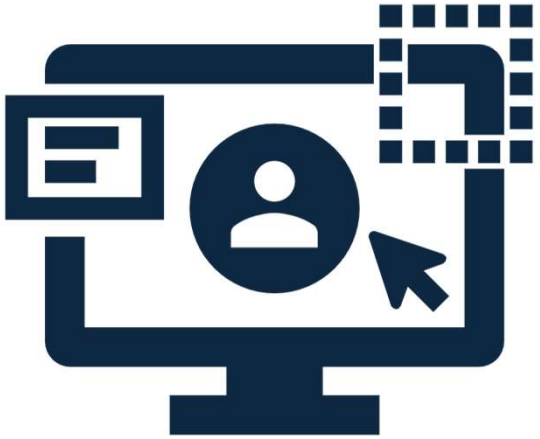

Brief Description

This portfolio highlights the end-to-end Microsoft Fabric implementation, covering data ingestion, transformation, governance, semantic modeling, and Power BI reporting. It includes architecture decisions, challenges solved, and business value delivered.

Pain Points / Challenges Before Implementation

- Unstable and slow refreshes when using large Excel files directly in Power BI.
- High memory consumption and refresh failures.
- Fragile schema—small changes break data refresh.
- Limited scalability of Excel beyond ~100k–300k rows.
- No governance, poor lineage, and repeated Power Query logic.
- No incremental refresh capability due to Excel acting as a monolithic blob.



Tools & Techniques

- Microsoft Fabric (Dataflows Gen2, Lakehouse, Pipelines, Notebooks)
- Power BI (Semantic model, DAX, Visualization, Control Tower)
- SharePoint + Power Automate for ingestion workflows
- SQL Endpoint for enterprise querying
- Delta Lake for scalable storage
- Python for data cleaning and automation when required



Value Creation



- Improved data reliability, governance, and traceability.
- Faster and stable dataset refresh cycles.
- Reusable transformation logic reduces maintenance.
- Single source of truth ensures KPI alignment across teams.
- Scalable architecture supports growth to millions of rows.
- Better decision-making via ***Digital Control Tower*** dashboards.

Microsoft Fabric Data Engineering and Analysis

Role: Digital Transformation & Data Expert | Industry: Construction & Project Management

As a Digital Transformation & Data Expert on a large-scale construction project, I Led the development of an automated, Fabric-powered Project Progress Dashboard that improved real-time visibility, standardized reporting, and streamlined data refresh workflows across the project.

📌***Key Contributions***:

- Designed a dynamic dashboard to track project KPIs
- Automated data ingestion using Power Automate → SharePoint List → Fabric Pipeline
- Modeled and transformed data using Fabric Lakehouse, SQL, and DAX
- Delivered weekly/monthly visual insights for engineering, planning, and construction teams
- Implementation of Digital Advance Work Package (AWO) on large scale project.


✨***Tools & Techniques:***

Power BI, Microsoft Fabric (Dataflows Gen2, Lakehouse, PySpark, Notebook, Pipeline, ETL, Medallion Architecture), Power Automate, SQL, DAX, Power Query


📈***Value Creation:***

- Improved project visibility and data reliability.
- Automated refresh pipeline reduced reporting time by 50%.
- Enabled a single source of truth for all project KPIs.


Fabric Data Architecture

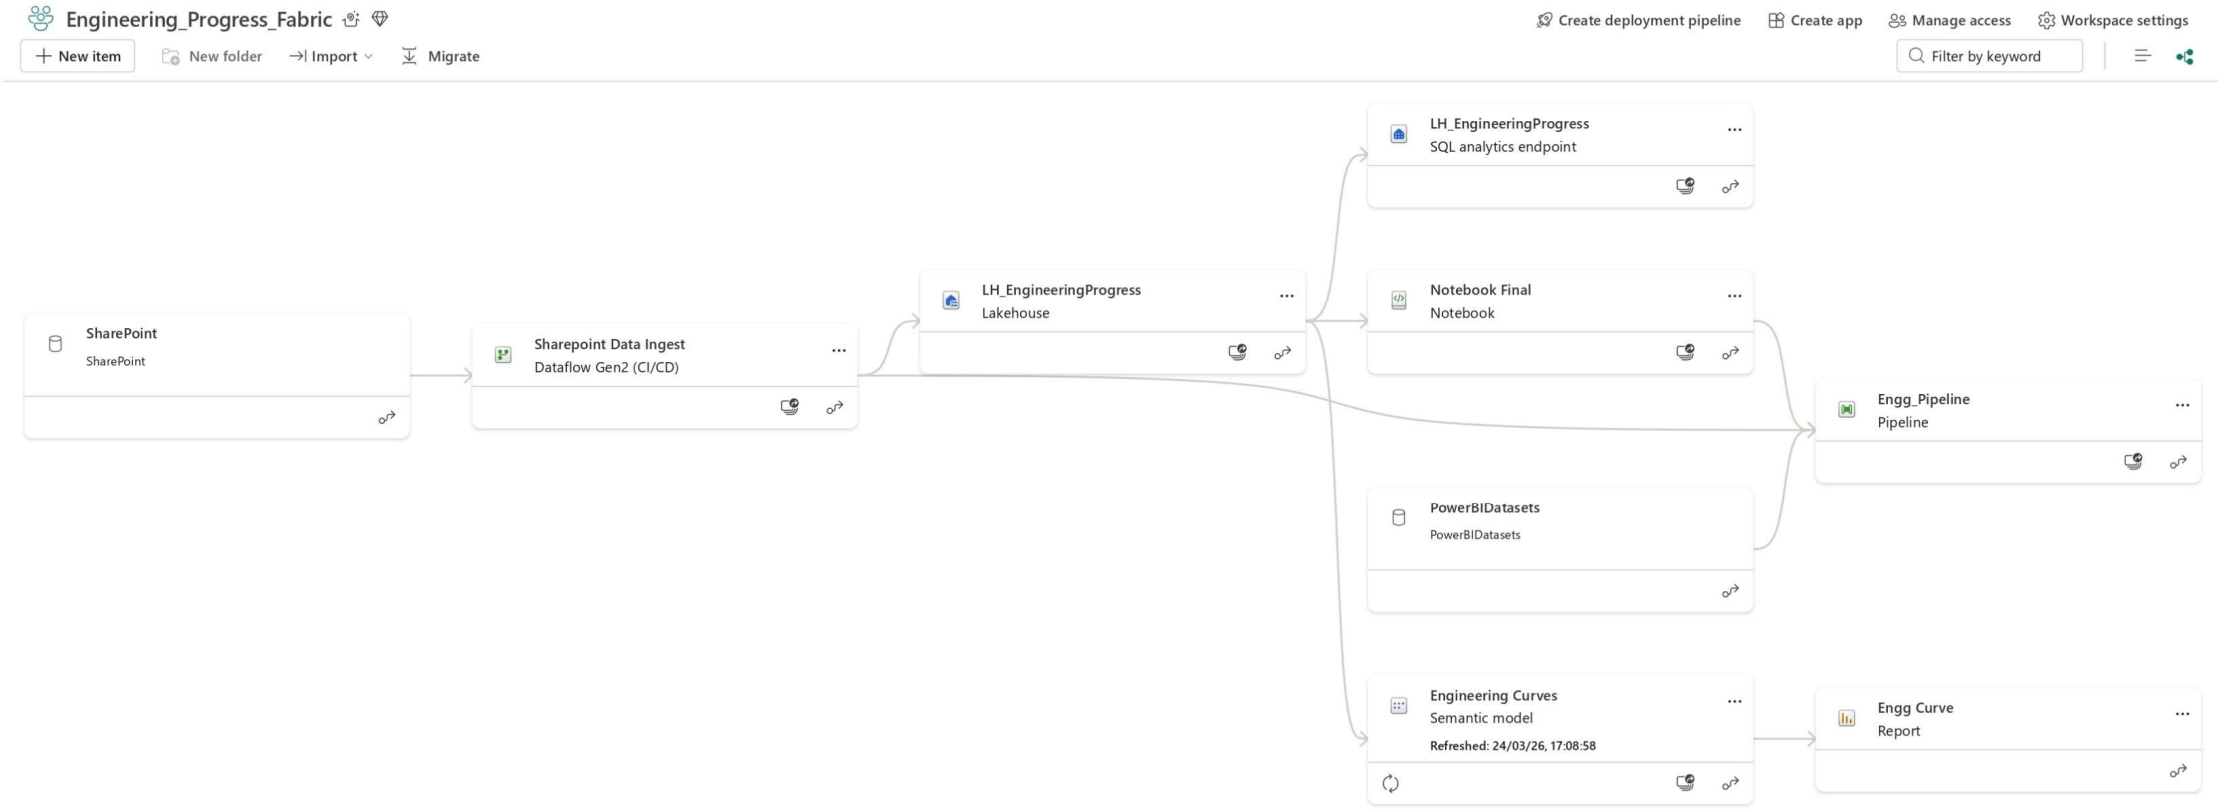


Data Pipeline Flow

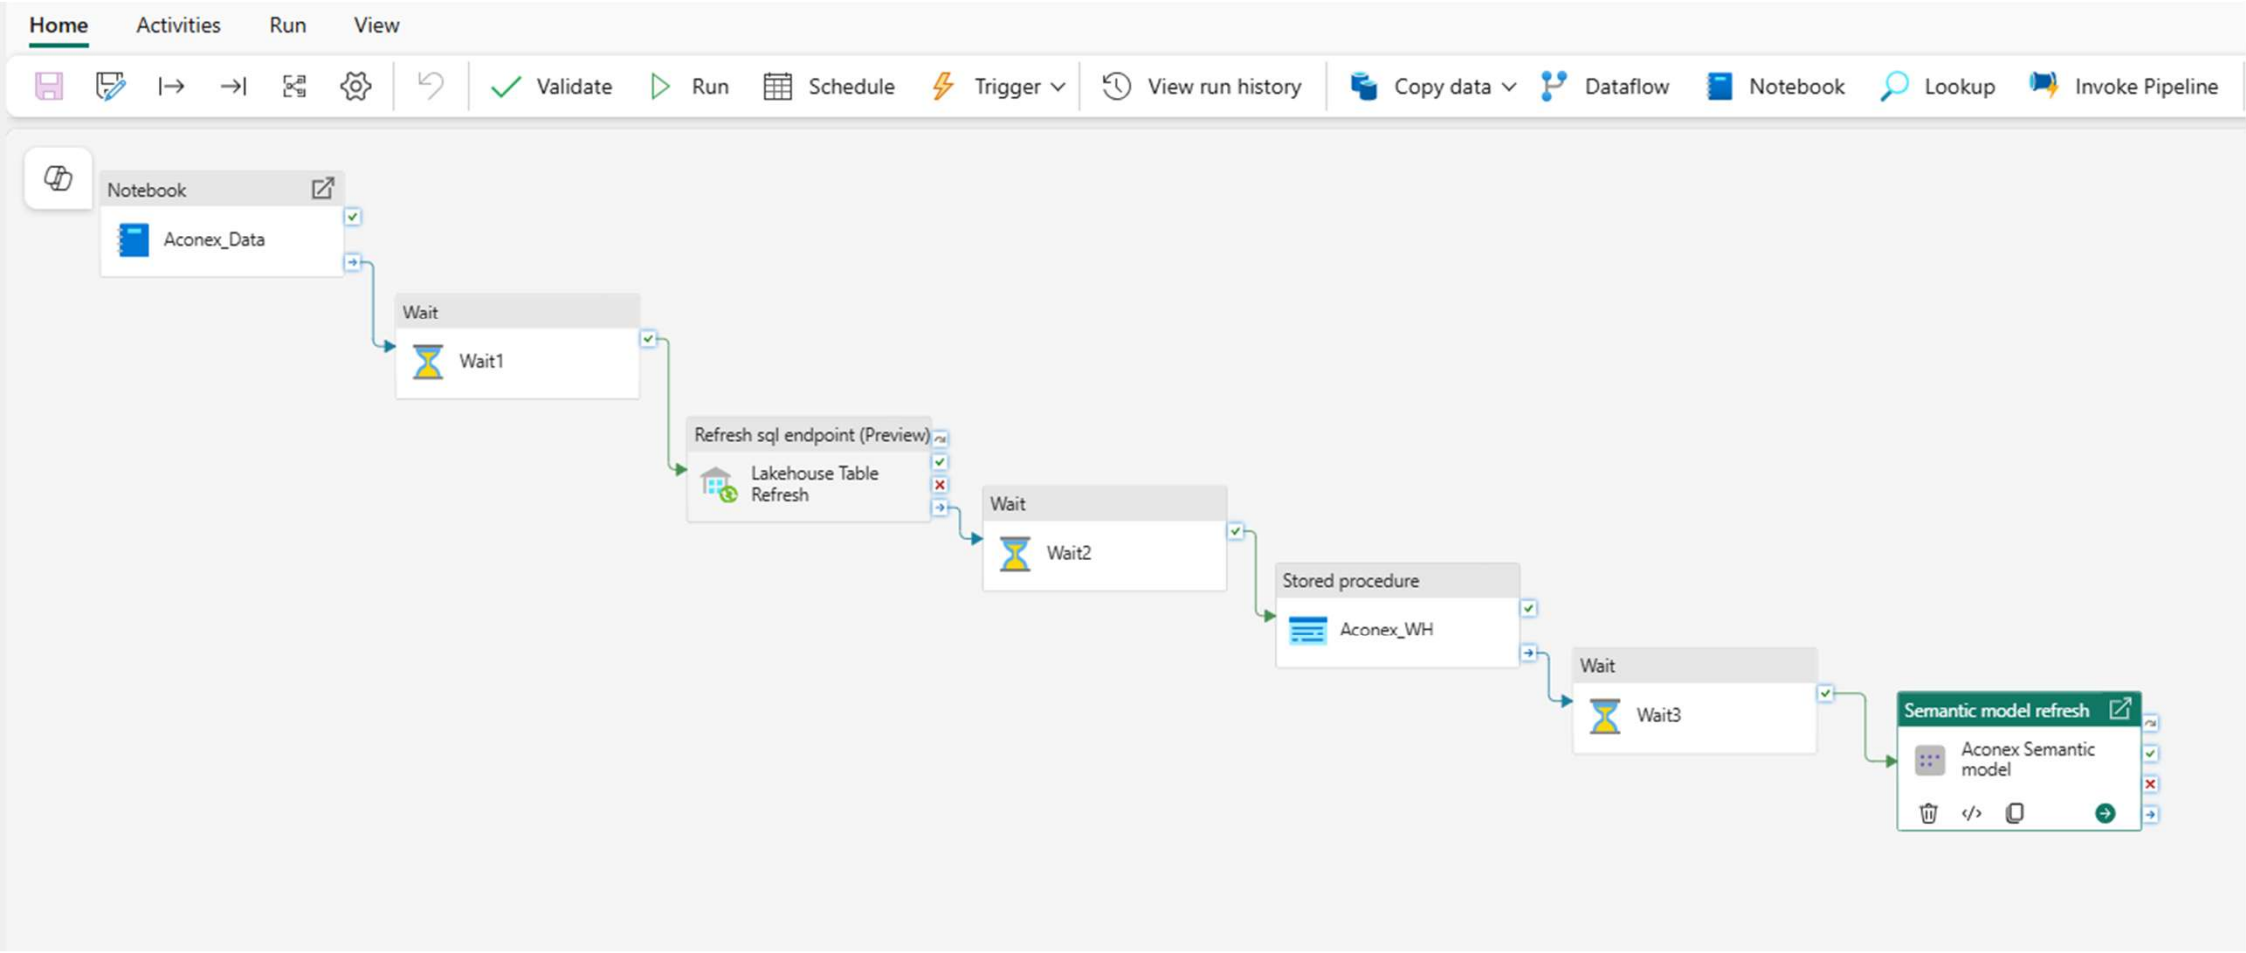


Microsoft Fabric Architecture with Medallion Model

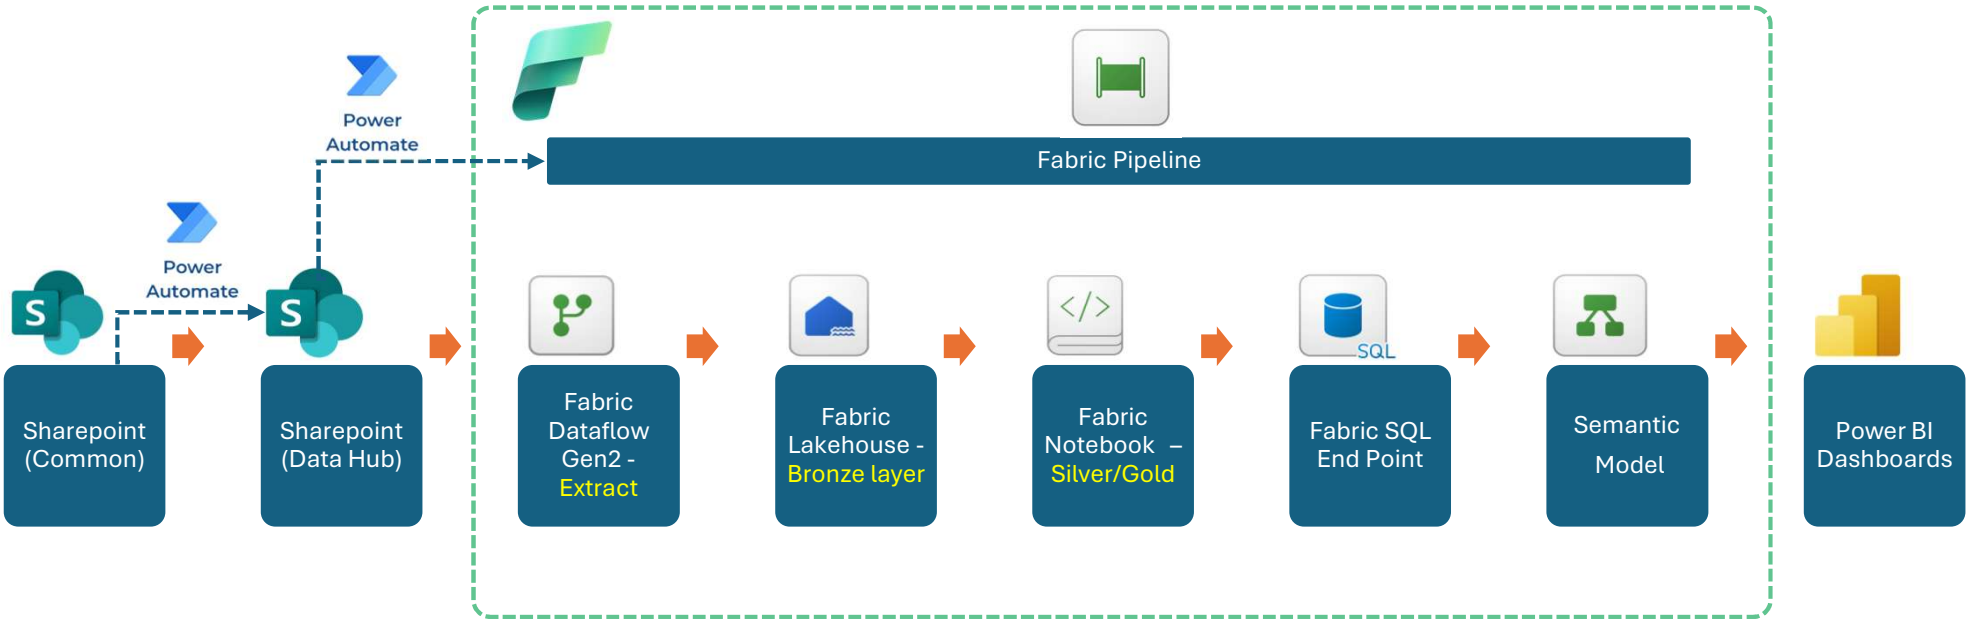


Flows & Triggers: Power Automate

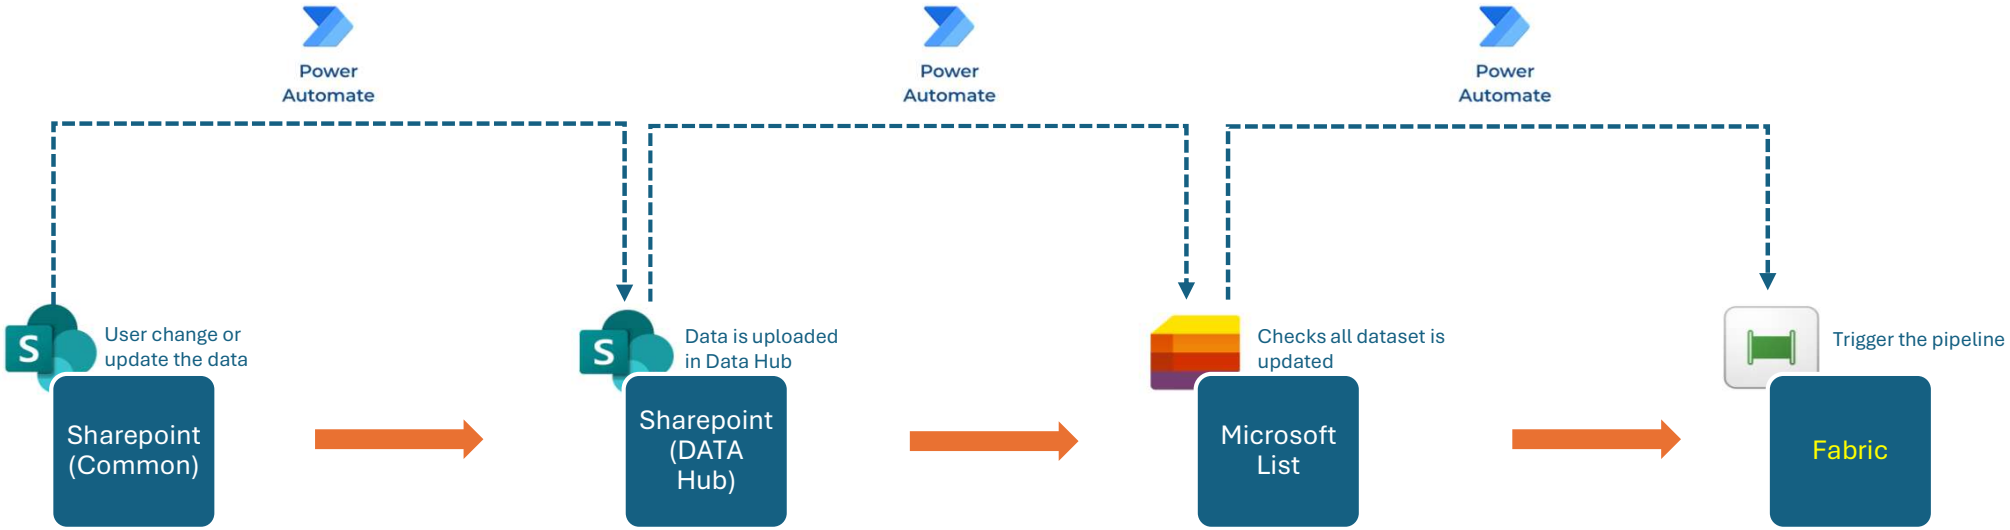


Power Automate Flow

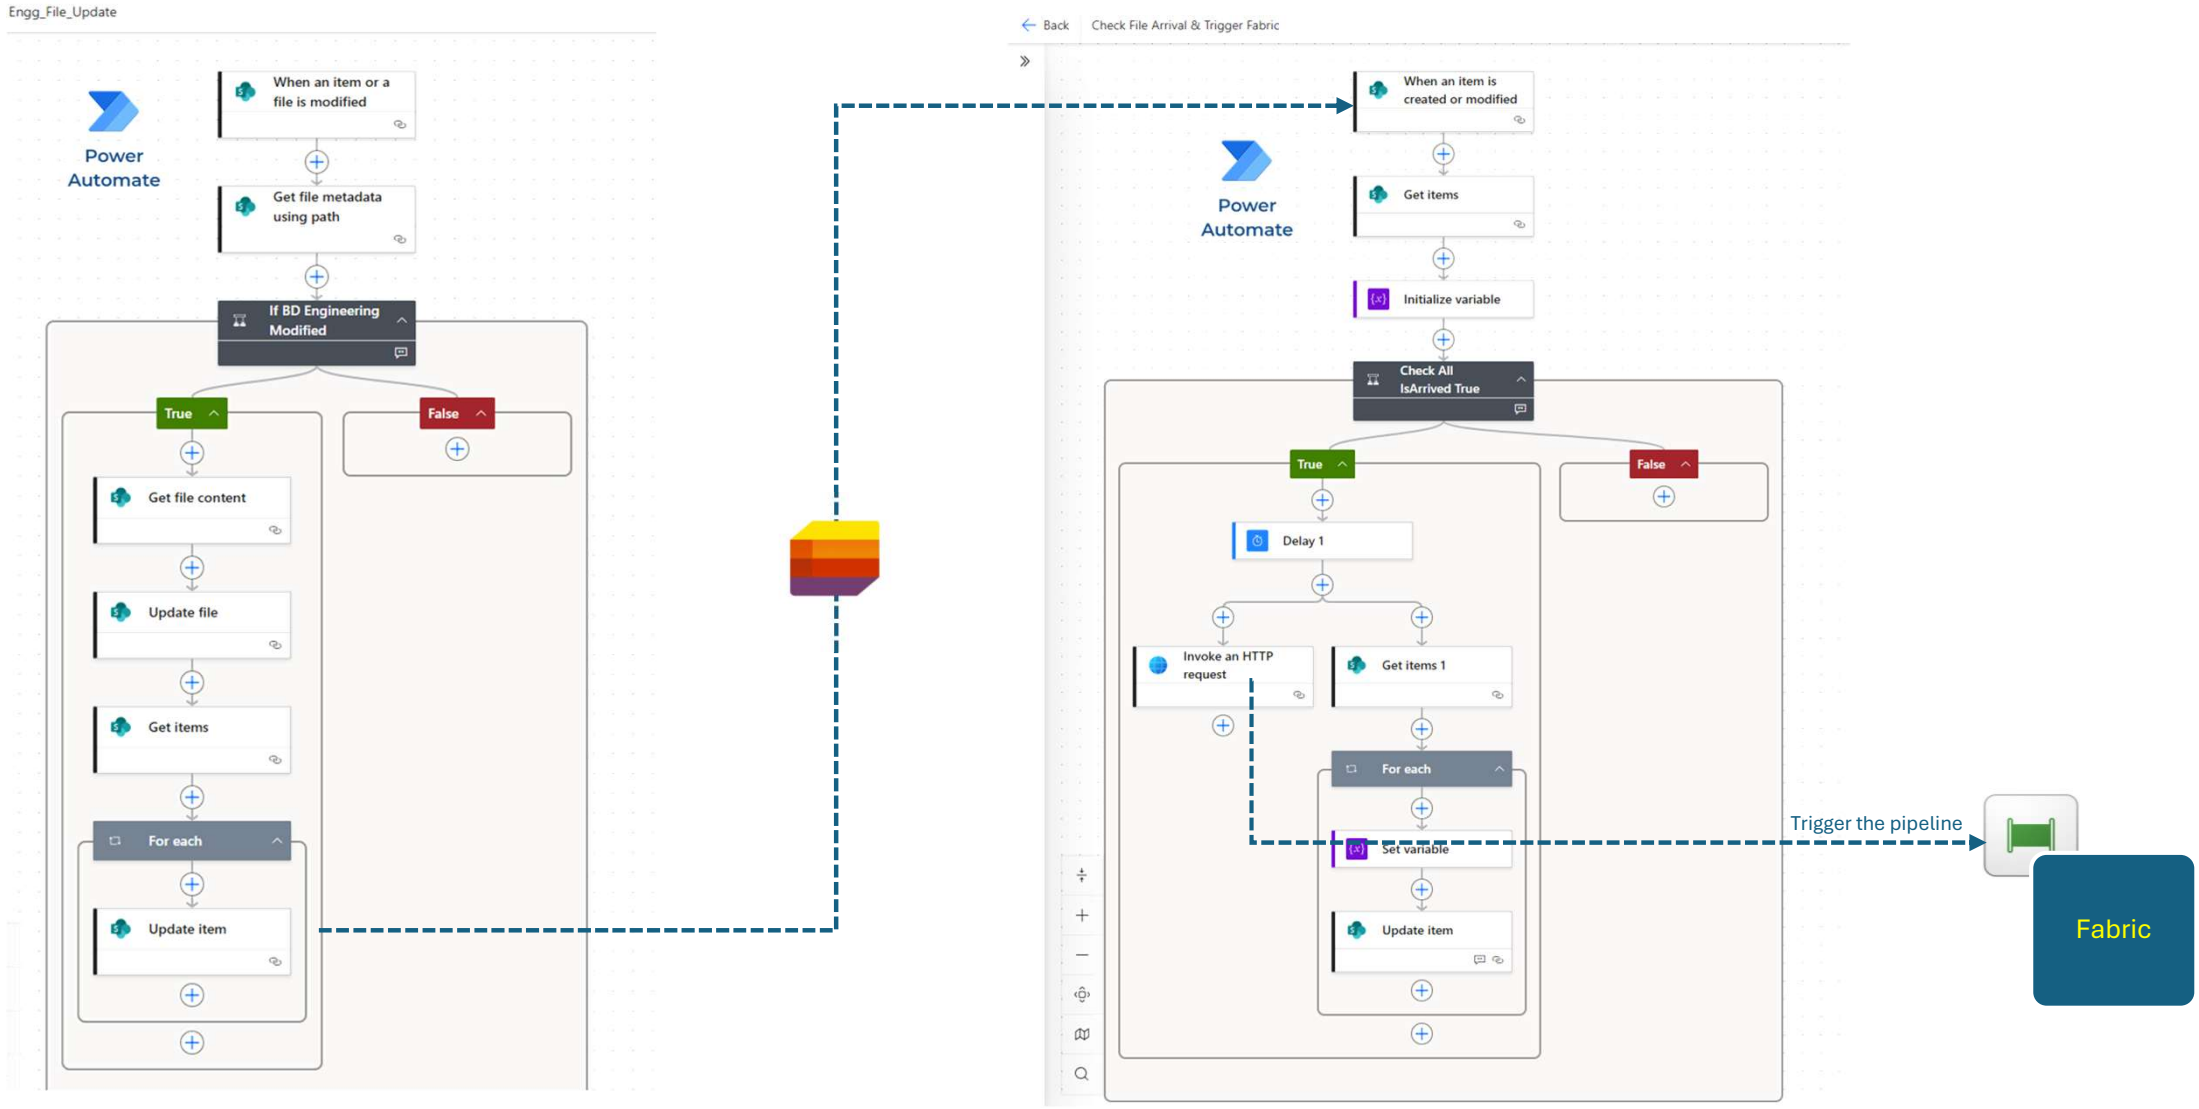

Digital Control Tower

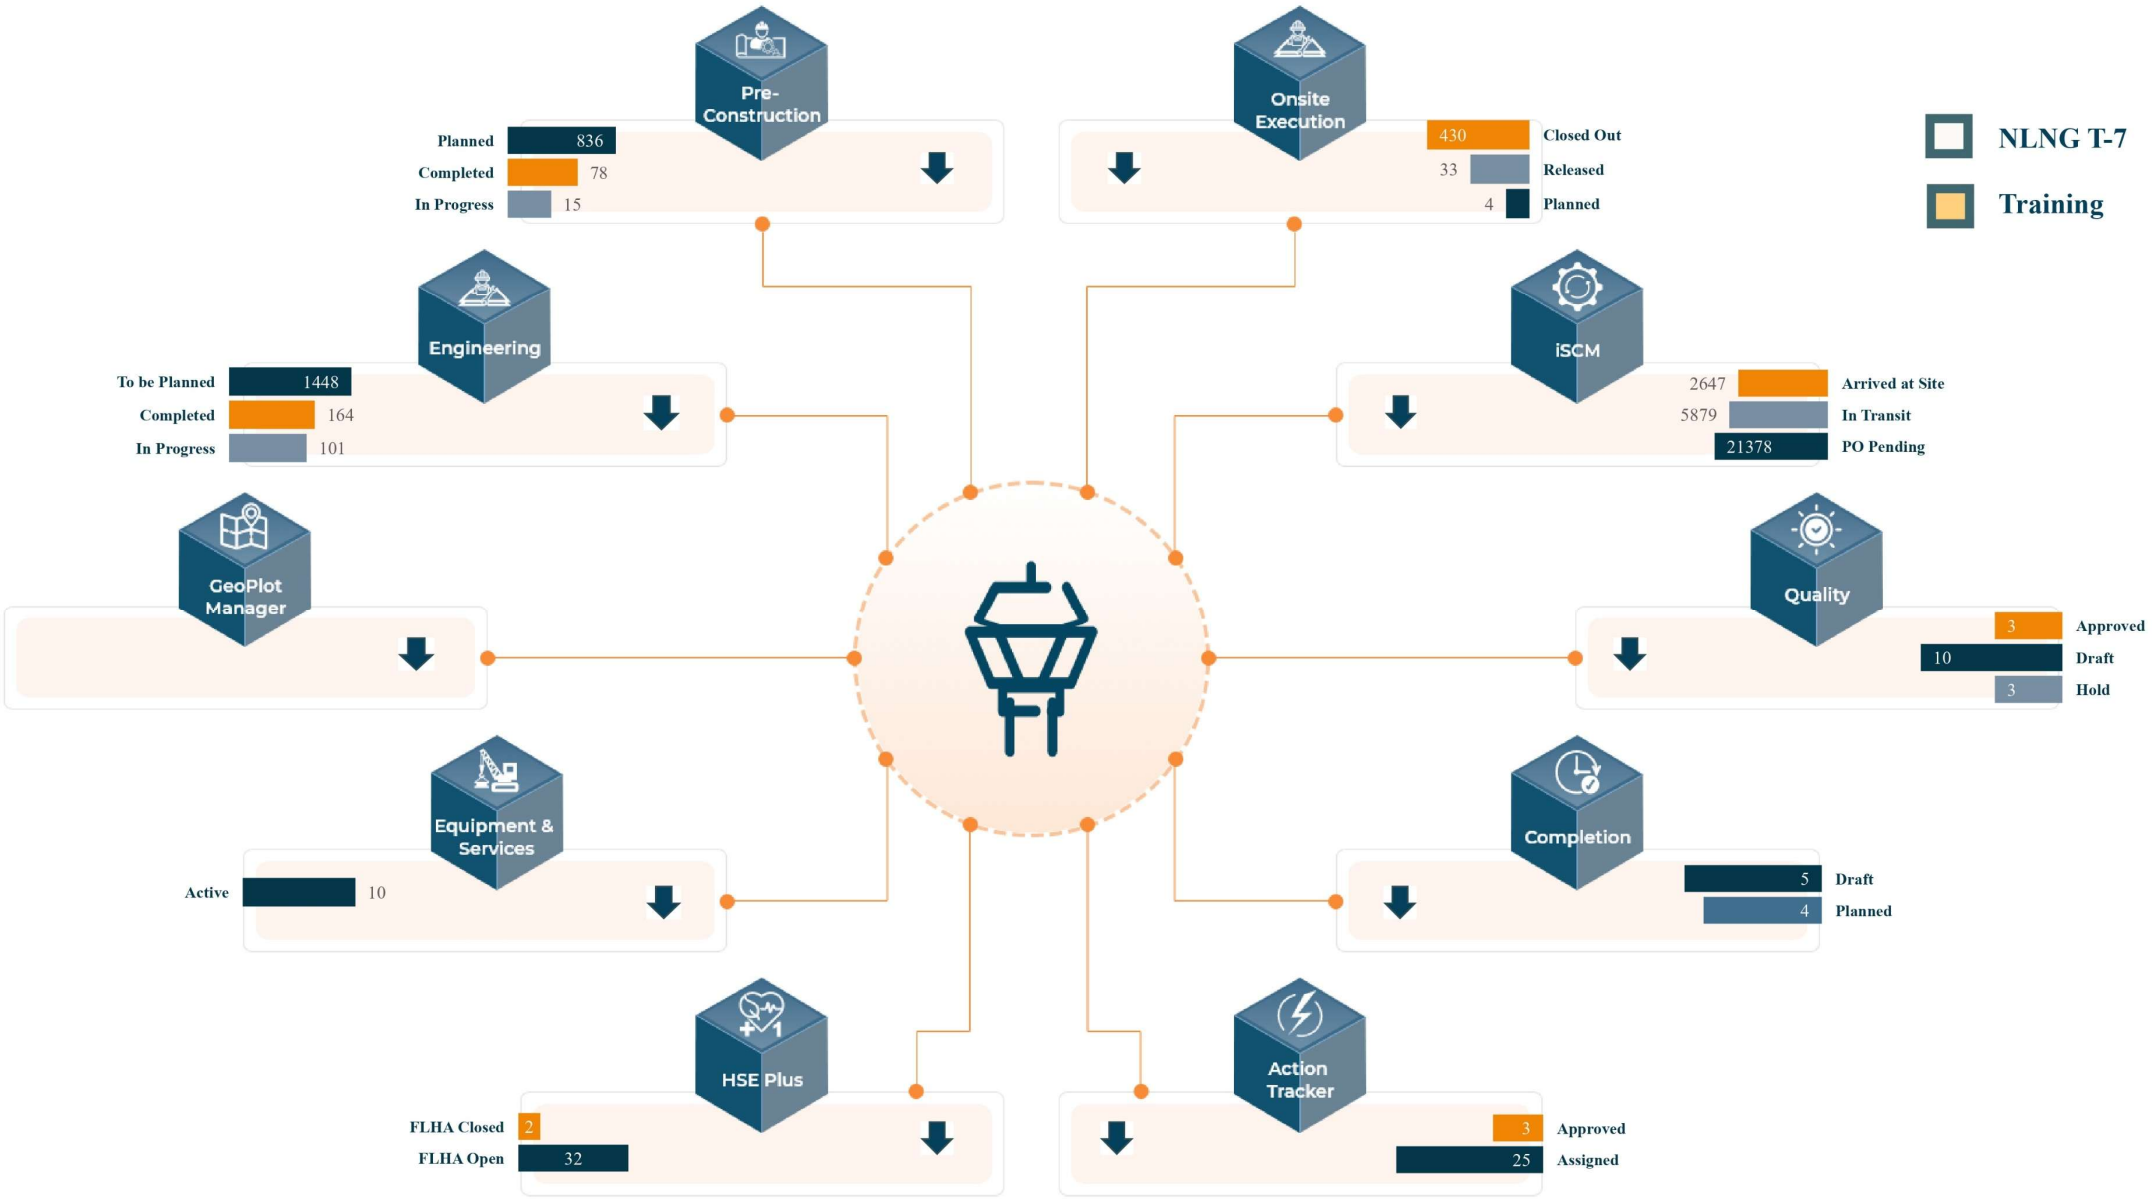

Digital Control Tower

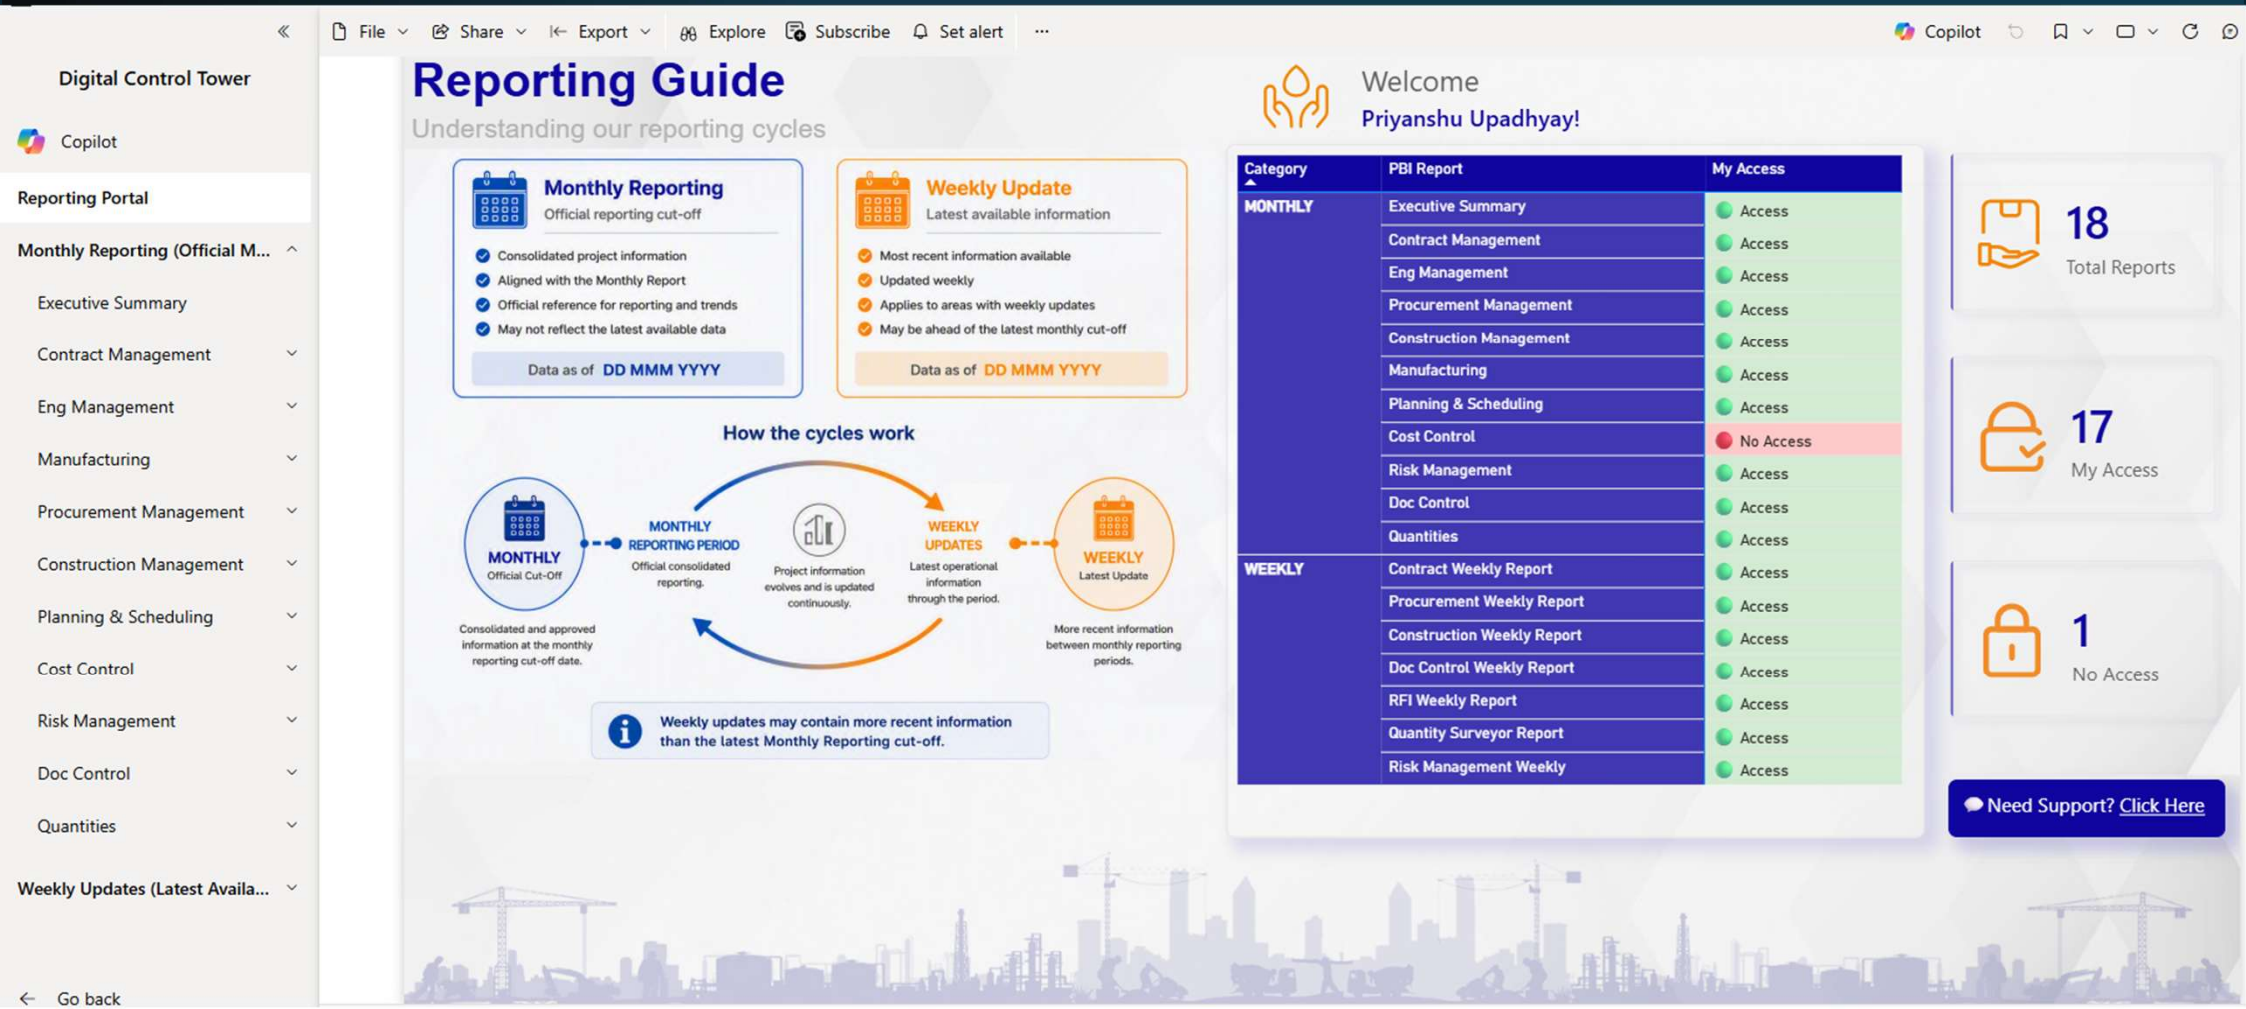

Digital Control Tower

Home / Planning & Scheduling

Planning & Scheduling Reports

Select a report to continue

Monthly Reporting
Official reporting cut-off
Data as of **30-Sept 2026**




Advance Work Package (AWP)



IWP Field Intelligence

CWP	Discipline	Status	IWP
All	Civil-General	Multiple selections	All

Delay Matrix

Area	CWP	Discipline	IWP	IWP Type	Stage	Status	Site Image	Planned Earned Q'ty	Actual Earned Q'ty (at Site)	UOM	Planned IWP EMH	Spent MH(PACE)	IWP-PlannedSta
Holding Basin_A06	CWP-A06-WP5.4-000-FI-LC-101	Civil-General	IWP-A06-WP5.4-000-FI-LC-101-CV01-101	Excavation / Backfill	Closed Out	Completed		16,882.14	16,882.14	M3	50646	14130	20 December 2022
Flare Area_A03	CWP-A03-WP5.3-000-FI-LC-101	Civil-General	IWP-A03-WP5.3-000-FI-LC-101-CV02-102	Concrete Work	Closed Out	Completed		1,106.67	1,080.00	M3	41979	15960	13 March 2023
Common Liquefaction Unit_A02	CWP-A02-WP2.4-220-CI-LC-103	Civil-General	IWP-A02-WP2.4-220-CI-LC-103-CV02-102	Concrete Work	Closed Out	Completed		1,063.49	1,063.49	M3	41782	12280	24 January 2023
New Complete Train_A01	CWP-A01-WP2.3-210-CI-LC-103	Civil-General	IWP-A01-WP2.3-210-CI-LC-103-CV02-102	Concrete Work	Closed Out	Completed		971.06	951.06	M3	38269	12940	16 March 2023

Project Progress Dashboard

Role: Digital Transformation & Data Analyst | Industry: Construction & Project Management

Led the development of a real-time Project Progress Dashboard that unified schedule, cost, manpower, and earned-value KPIs. The solution improved visibility, standardized reporting, and enabled faster decision-making across engineering, planning, and construction teams.

Key Contributions:

- Built a KPI-driven dashboard displaying progress to date, earned hours, plan vs actual, and performance factors.
- Integrated data from planning systems, cost controls, engineering deliverables, and construction progress feeds.
- Automated weekly/monthly reporting with trend charts, variance analysis, and manpower curves.
- Implemented validation rules and consistent business logic to ensure accurate KPI alignment.
- Collaborated with planners and cost controllers to map analytics to field and PMO workflow

Tools & Techniques:

Power BI, SQL, DAX, Power Query, Earned Value Management (CPI, SPI, PF)

Value Creation:

- Delivered a single source of truth for project performance.
- Improved reporting accuracy and progress transparency across all disciplines.
- Reduced manual reporting time by 50%, enabling teams to focus on insights instead of data preparation.
- Strengthened decision-making with clear plan vs actual insights and predictive trends.

Project Progress Dashboard

Project | By Building | % Building | Progress Table Overall | SC Dashboard | SC Manpower | Project - S Curve | Qty-Curve | Variation Curve

Progress to Date



Earned Hours

26,25,017 ✓

Planned Hours: 26,24,952 (+0%)


Project PF



Building	Weight	Control Budget Hours	Spent Hours	Earned Hours	PF	% Cmplt	% Plan to Date	Delta %
Headblock	12.25%	4,57,272	3,85,226	3,26,309	0.85	71.4%	70.9%	0.5%
DSM4	31.43%	11,72,728	11,16,615	9,11,678	0.82	77.7%	78.6%	-0.8%
DSM5	30.02%	11,19,562	5,55,515	5,66,274	1.02	50.6%	50.3%	0.3%
Warehouse	6.67%	2,49,267	1,71,714	1,74,063	1.01	69.8%	66.7%	3.1%
CUB	10.39%	3,85,729	4,05,324	3,33,270	0.82	86.4%	87.7%	-1.3%
Spine	2.19%	82,662	45,121	58,202	1.29	70.4%	67.5%	2.9%
Tank Farm	1.06%	39,901	30,509	31,124	1.02	78.0%	81.6%	-3.6%
Site	6.12%	2,26,807	1,90,018	2,24,097	1.18	99.8%	100.0%	-0.2%
Total	**100.00%**	**37,33,928**	**29,00,042**	**26,25,017**	**0.91**			

Week End	Inc. Spent Hrs.	Inc. Earned Hrs.	Inc. Planned Hrs.
27-Jun-25	55,411	47,219	52,281

Building	QVD Total	QVD Actual	QVD % Cmplt	W2 Total	W2 Actual	W3 Total	W3 Actual	MC Total	MC Actual	MC % Cmplt
Headblock	3942	264	6.7%	250	13	250	4	58	2	3.4%
DSM4	17050	4600	27.0%	1356	236	1356	142	333	10	3.0%
DSM5	10647	510	4.8%	1190	18	1190	14	330	4	1.2%
Warehouse	3303	35	1.1%	410	7	410	6	89	3	3.4%
CUB	6990	2535	36.3%	740	148	740	95	140	22	15.7%
Spine	1119	735	65.7%	66	21	66	19	24	11	45.8%
Tank Farm	894	135	15.1%	90	2	90	1	20	1	5.0%
Site	56	45	80.4%	11	2	11	2	4	1	25.0%
Total	**44001**	**8859**	**20.1%**	**4113**	**447**	**4113**	**283**	**998**	**54**	**5.4%**

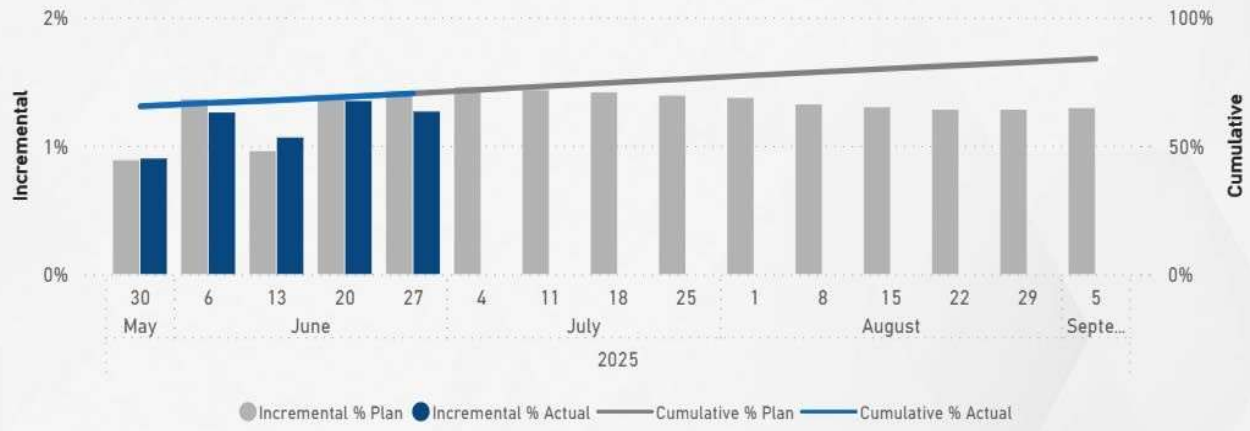

Year	2025															
Month	May	June				July				August						September
	30	6	13	20	27	4	11	18	25	1	8	15	22	29	5	
Plan % Cumulative	65.2%	66.6%	67.5%	68.9%	70.3%	71.8%	73.2%	74.6%	76.0%	77.4%	78.7%	80.0%	81.3%	82.5%		83.8%
Actual % Cumulative	65.4%	66.6%	67.7%	69.0%	70.3%											
Plan % Incremental	0.9%	1.4%	1.0%	1.4%	1.4%	1.5%	1.4%	1.4%	1.4%	1.4%	1.3%	1.3%	1.3%	1.3%		1.3%
Actual % Incremental	0.9%	1.3%	1.1%	1.3%	1.3%											

Plan & Actual by Week



Year	2025															
Month	May	June				July				August						September
	30	6	13	20	27	4	11	18	25	1	8	15	22	29	5	
Plan Manpower	723	1097	763	1081	1120	1429	1212	1127	1103	1091	1054	1035	1026	1028		1035
Actual Manpower	1159	1233	1186	1415	1228	0	0	0	0	0	0	0	0	0		0

Building/Unit Area Report

Developed a detailed progress tracking report for the building/unit area level , enabling visibility into contractor performance and earned value metrics.

Key Contributions:

- Tracked 42.4% completion with SPI of 0.75
- Created contractor-level earned value tables
- Visualized monthly incremental and cumulative progress

Tools & Techniques:

SQL, DAX, Power BI, Power Query, Earned Value Analysis

Value Creation:

Enabled early intervention and improved contractor accountability

Building/Unit Area Report

Project | By Building | % Building | Progress Table Overall | SC Dashboard | SC Manpower | Project - S Curve | Qty-Curve | Variation Curve

Contract	Contractor	Weight	Control Budget Hours	Spent Hours	Earned Hours	Inc. Plan	Inc. Earned	Delta Hrs.	% Cmplt	Plan to Date	Delta %
K002 Piling	Per Aarsleff	0.62%	7,222	9,390	7,218	0		0	100.0%	100.0%	0.0%
K003 Pile Caps (DSM4, CUB)	NCC	2.36%	27,700	16,364	27,705	0		0	100.0%	100.0%	0.0%
K010 Concrete Package East	Per Aarsleff	3.69%	43,777	50,869	43,777	0	0	0	100.0%	100.0%	-0.0%
K020 Structural Steel	CSK	3.09%	37,058	38,876	37,429	0	0	0	100.0%	98.6%	1.4%
K030 Roofing and Cladding	Kai Andersen	2.28%	26,783	18,565	23,080	186	0	-186	86.2%	82.4%	3.8%
K031 Clean Rooms	KCS	4.17%	48,865	36,774	34,098	979	920	-59	69.8%	74.1%	-4.3%
K032 Architecture - East	Ardmac	12.31%	1,44,335	1,08,305	1,20,488	2,081	550	-1,531	83.5%	83.4%	0.1%
K036 Lab casework	ZYSTM	0.12%	1,351	0	0	0	0	0	0.0%	0.0%	0.0%
K040 Lifts and Dumbwaiters	Schindler	0.09%	1,000	502	900	0	0	0	90.0%	90.0%	0.0%
K041 Cold Rooms / Freezers	Lowenco	1.02%	11,927	16,110	10,529	0	45	45	88.3%	96.6%	-8.3%
K045 HVAC East	Dornan HVAC	4.15%	48,648	55,355	35,933	529	670	141	73.9%	80.5%	-6.6%
K050 Pipe Racks East	Mercury	3.01%	35,331	76,197	33,897	0	995	995	95.9%	100.0%	-4.1%
K051 UG Process Drain	Jones	1.10%	12,913	8,821	12,911	0	0	0	100.0%	100.0%	0.0%
K053 Fire Protection	Bravida	2.30%	26,973	28,987	23,770	109	193	84	88.1%	88.5%	-0.4%
K055 Utility Piping East	Zauner	8.54%	1,00,188	2,03,886	90,367	411	650	239	90.2%	85.5%	4.7%
K057 Hygenic Piping	Jones	8.88%	1,04,109	92,208	90,949	985	1,820	835	87.4%	85.4%	1.9%
K059 Passivation & Flushing	Jones	2.93%	34,343	2,524	3,216	382	451	69	9.4%	1.4%	8.0%
K061 E&I - DSM4	Dornan E&I	20.93%	2,45,475	2,56,019	1,47,249	6,984	4,107	-2,877	60.0%	66.4%	-6.5%
K064 Electrical HV Contract	Bravida	0.01%	110	110	110	0	0	0	100.0%	100.0%	0.0%
K070 Fire Alarm	Bravida	1.28%	14,993	14,235	9,727	296	182	-114	64.9%	67.8%	-3.0%
K071 BMS & EMS	Eltronic	1.53%	17,960	12,332	6,659	834	412	-422	37.1%	58.7%	-21.7%
K072 Security Infrastructure	Bravida	0.55%	6,436	5,096	2,394	30	39	9	37.2%	10.1%	27.1%
K074 IT Systems	STS	0.82%	9,572	1,876	3,059	305	503	198	32.0%	21.6%	10.4%
K080 Equipment Move-in	Jones	4.08%	47,850	32,310	45,367	67	0	-67	94.8%	95.8%	-1.0%
K082 Fire Stopping	FireStop	5.85%	68,640	30,904	59,021	753	753	0	86.0%	84.4%	1.6%
V101 Variations	--	4.31%	49,169		41,825	688	688	0	77.9%	78.4%	-0.5%
Total		**100.00%**	**11,72,728**	**11,16,615**	**9,11,678**	**15,619**	**12,978**	**-2,641**			

Progress to Date



Earned Hours


9,11,678 !

Planned Hours: 9,21,530 (-1.07%)

SPI (Including variation)



Year	2025									
Month	May	June				July				August
	30	6	13	20	27	4	11	18	25	1
Plan % Cumulative	73.7%	75.0%	75.9%	77.2%	78.6%	80.0%	81.4%	82.8%	84.2%	85.5%
Actual % Cumulative	73.6%	74.5%	75.4%	76.6%	77.7%					
Plan % Incremental	0.8%	1.3%	0.9%	1.3%	1.3%	1.4%	1.4%	1.4%	1.4%	1.4%
Actual % Incremental	→ 0.8%	↓ 0.9%	→ 0.9%	↓ 1.2%	↓ 1.1%					

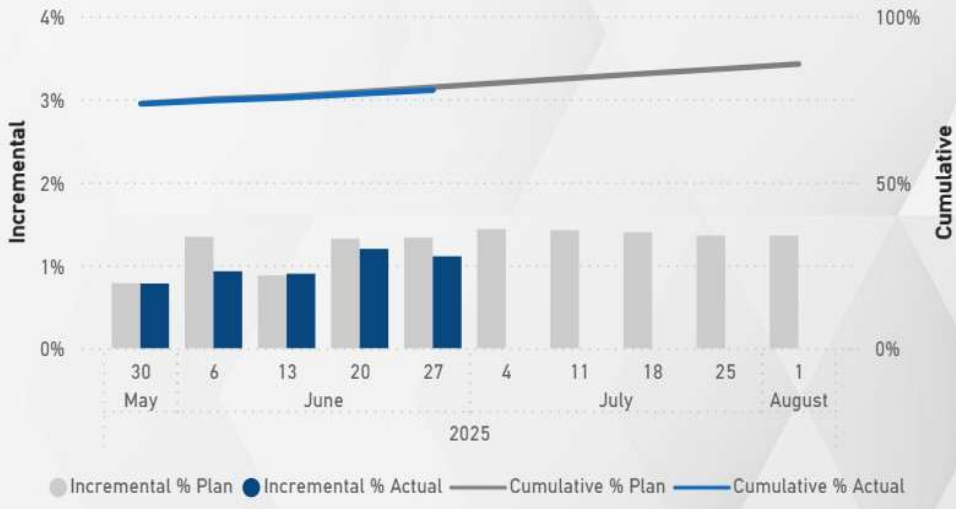

Contractor Detail Report – Status Report

Developed a status report for the 20+ Contractors working on a project, providing insights into progress, resource utilization, and schedule performance.

Key Contributions:

- Developed weekly plan vs actual progress tables
- Tracked FTE utilization and milestone dates
- Built variation and billing tables by department

Tools & Techniques:

SQL, DAX, Power BI, Power Query, ,Variance Analysis

Value Creation:

Improved schedule clarity and supported scope management

Contractor Detail Report – Status Report

Project Status

K032 Architectural Finishes East

21 Feb 2025

Date - Week Ending

EXECUTIVE SUMMARY

- HB - Achieved 1,029m2 combined 1st & 2nd Fix
- HB - Detailed Plan has been agreed to achieve Week 10 Milestone Combined Wall Quantity of 18,500m2
- DSM5 - on track to reach agreed quantities

Building	Budget Hours	Cum. Plan Hours	Cum. Spent Hours	Cum. Earned Hours	Cum. PF Building Excl. Variations	Cum. Plan %	Cum Actual %	% Delta	Inc. Plan Hours	Inc. Spent Hours	Inc. Earned Hours
Headblock	67,158	35,287	56,997	31,551	0.55	52.5%	47.0%	-5.6%	51	4,013	2,048
DSM4	84,764	58,282	87,963	61,209	0.70	68.8%	71.3%	2.5%	97	1,512	712
DSM5	84,885	41,306	41,941	39,101	0.93	48.7%	46.1%	-2.6%	2,346	1,816	1,062
Total	**236,807**	**134,875**	**186,901**	**131,861**	**0.71**				**2,494**	**7,341**	**3,822**

Concerns/Challenges

- DSM4 -committed to increase to 18 wall fixers
- DSM5 still not provided 30 fixers as promissed
- HB insufficient supervision is impacting productivity and target quantities not being achieved.


Variation

Category	Approved Variation Hours	Potential Variation Hours	Total Variation Hours	Earned Hours
	26,106	22,335	48,441	0
Modification of existing progress items	14,786	13,826	28,612	20,882
Total	**41,905**	**36,301**	**78,206**	**21,895**

K032 - Total Progress



Plan & Actual by Week

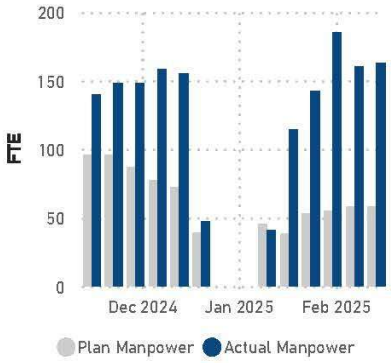

Progress vs Plan (Base Scope)



SPI (Cumulative)



Progress (Base Scope + Variations)



PF (Cumulative)



SPI Trend →

PF Trend →

Key Quantities

Building	Quantity Type	Unit	Plan Total	Cum. Plan	Cum. Installed	Inc. Plan	Inc. Installed
Headblock	Ceiling	m2	7,857	1,736	0	306	0
Headblock	Flooring	m2	10,783	299	5,517	80	0
Headblock	Walls	m2	23,715	15,901	14,832	710	1,028
DSM4	Ceiling	m2	1,716	476	172	0	0
DSM4	Flooring	m2	11,660	11,560	10,363	0	0
DSM4	Walls	m2	25,282	20,940	23,161	220	391
DSM5	Ceiling	m2	1,722	181	0	0	0

Key Dates

Building	Milestone	Plan Start	Fcst. Start	Act. Start	Plan Finish	Fcst. Finish	Act. Finish	Delta
Headblock	Ceilings	17-Oct-24		18-Feb-25	06-Aug-25	11-Aug-25		
DSM4	Ceilings	06-Jan-25		21-Nov-24	16-Sep-25	25-Nov-25		
DSM5	Ceilings	07-Aug-25	06-May-25		28-Jan-26	24-Mar-26		
Headblock	Flooring	01-Aug-24		02-Sep-24	06-Aug-25	26-Aug-25		
DSM4	Flooring	11-Dec-23		11-Dec-23	06-Dec-24		14-Feb-25	

Project Trend Analysis – Base Scope + Variation

Key Contributions:

- Modeled incremental and cumulative hours over 4 years
- Forecasting & Trend Modeling and Data Visualization.
- Time-Series Data Structuring and Strategic Reporting.
- Supported long-term planning and resource forecasting


Tools & Techniques:

SQL, DAX, Power BI, Power Query, Time-Series Analysis

Value Creation:


Improved timeline clarity by 40% and enabled proactive planning

Project Trend Analysis – Base Scope + Forecast

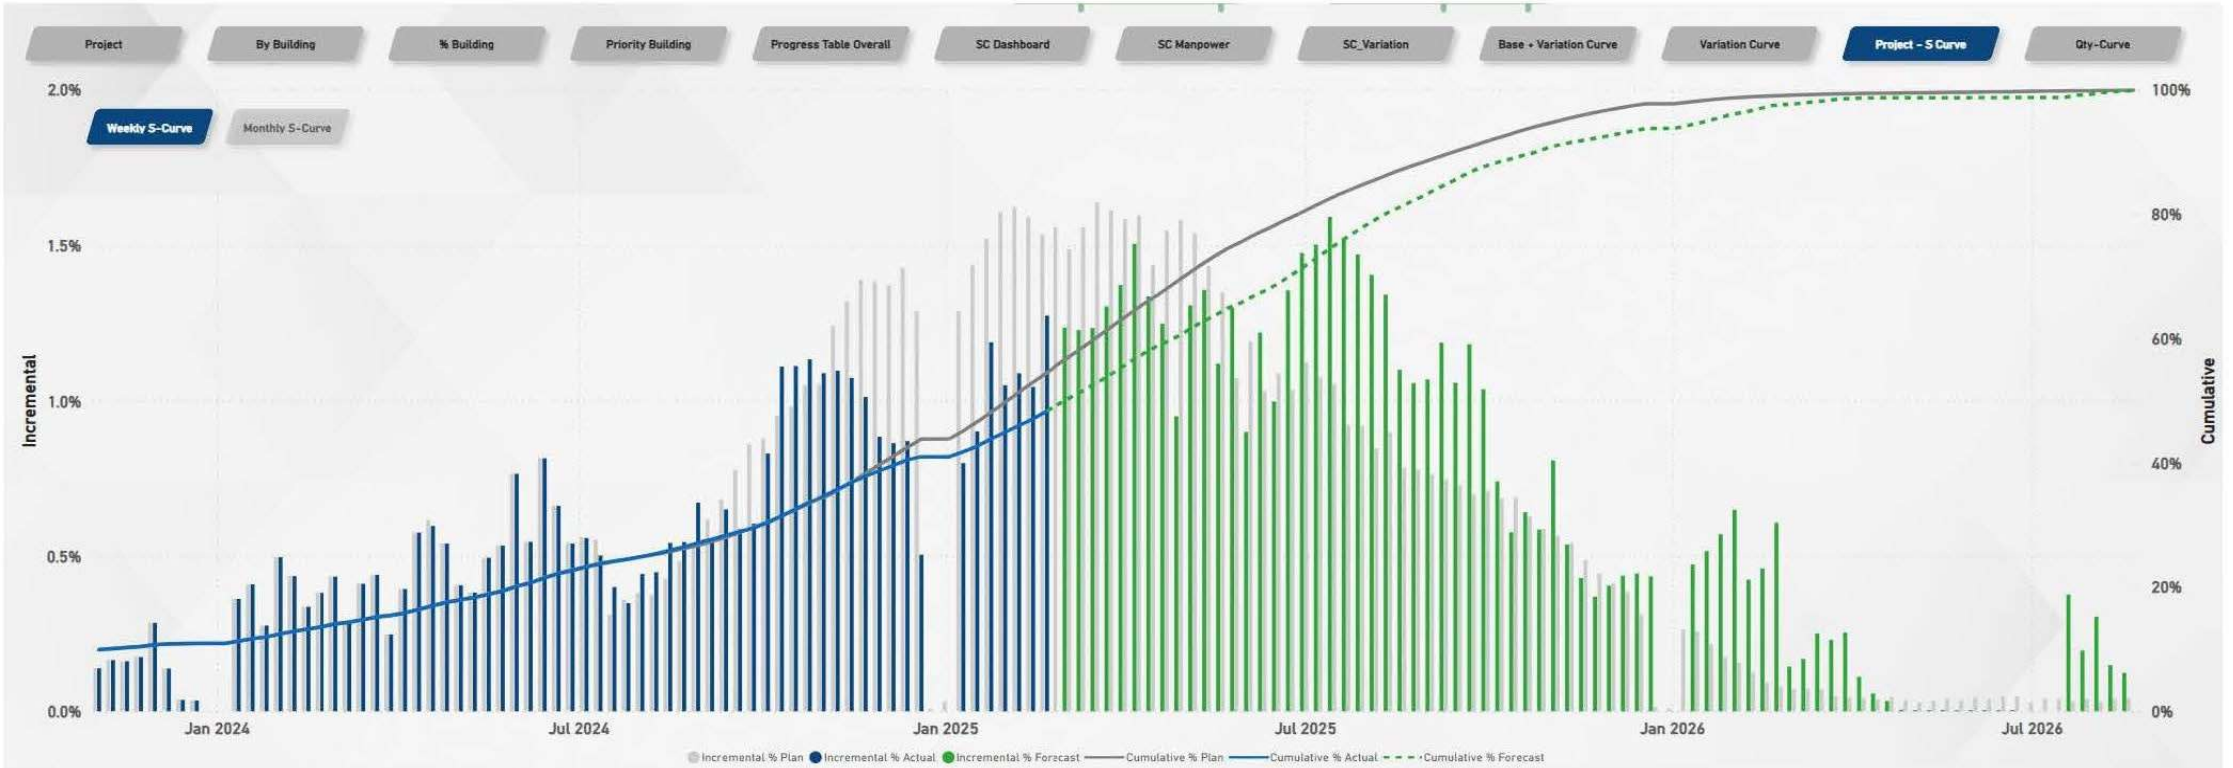

| Year | 2024 | | | | | | | 2025 | | | | | | |

Project Trend Analysis – Base Scope + Variation

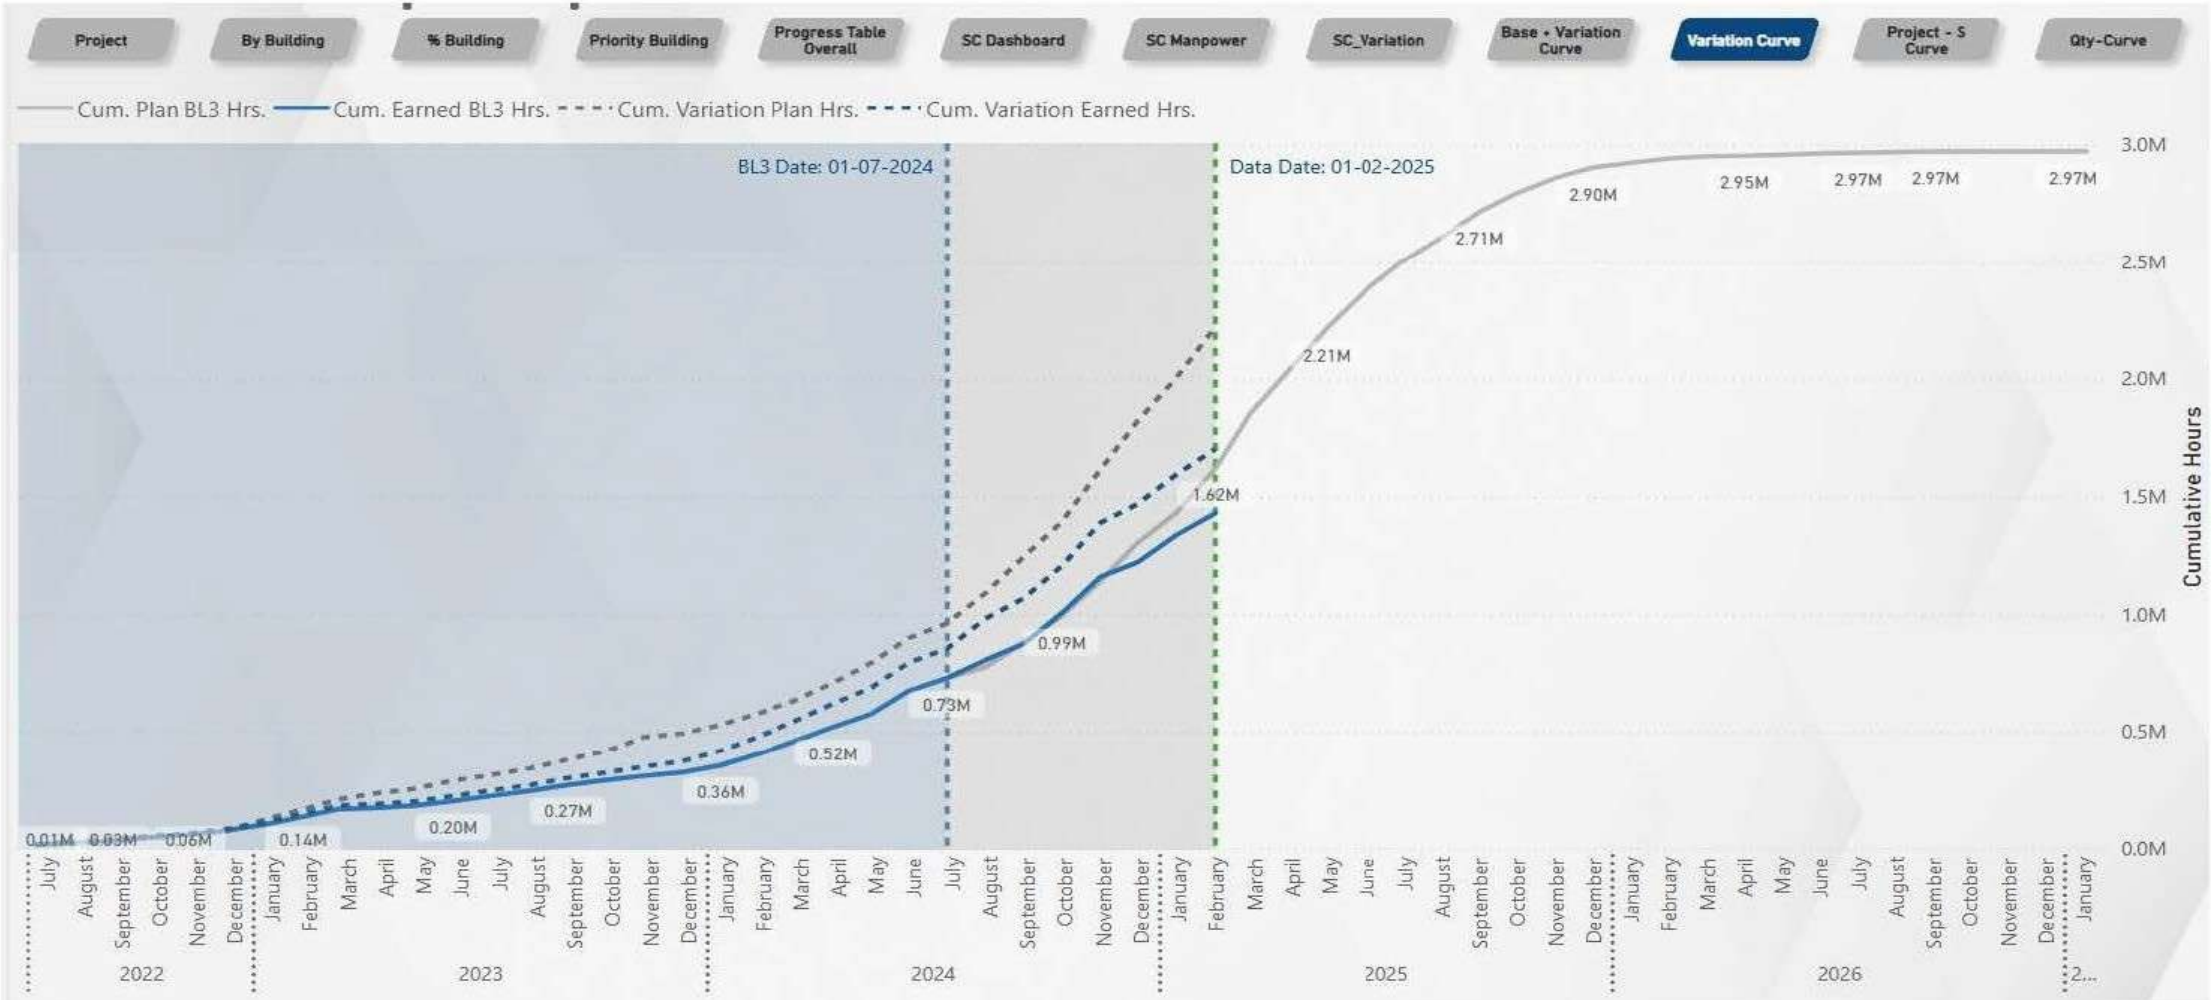

Year	2024												2025												2026	
	January	February	March	April	May	June	July	August	September	October	November	December	January	February	March	April	May	June	July	August	September	October	November	December	January	F
Inc. Plan BL3 Hrs.	30K	48K	53K	62K	53K	98K	53K	51K	101K	116K	149K	163K	128K	190K	235K	184K	175K	160K	125K	101K	110K	80K	65K	45K	21K	
Inc. Variation Plan	5K	2K	0K	12K	27K	11K	8K	81K	53K	33K	74K	45K	56K	27K												
Inc. Earned BL3 Hrs.	30K	48K	53K	62K	53K	98K	53K	59K	92K	128K	128K	92K	86K	92K												
Inc. Variation Earned	15K	12K	11K	13K	12K	9K	4K	51K	17K	8K	30K	18K	9K	16K												
Cum. Plan BL3 Hrs.	357K	404K	458K	520K	577K	675K	728K	775K	880K	993K	1,141K	1,305K	1,432K	1,620K	1,854K	2,039K	2,214K	2,375K	2,499K	2,600K	2,713K	2,794K	2,859K	2,904K	2,924K	
Cum. Variation Plan Hrs.	173K	175K	175K	187K	215K	225K	233K	314K	366K	399K	473K	518K	574K	601K												
Cum. Plan BL3+Variation Hrs.	529K	579K	633K	707K	791K	900K	961K	1,090K	1,246K	1,392K	1,614K	1,822K	2,006K	2,221K												

Weekly Manpower Tracking

Key Contributions:

- Workforce Variance Analysis and Contractor-Level Breakdown.
- Performance Monitoring and Data Accuracy & Reporting.
- Compared planned vs actual manpower weekly
- Created contractor-level workforce tables
- Identified under/over-resourcing trends

Tools & Techniques:

SQL, DAX, Power BI, Power Query, Workforce Analytics


Value Creation:

Reduced reporting errors by 25% and improved labor planning

Weekly Manpower Tracking

Project | By Building | % Building | Progress Table Overall | SC Dashboard | **SC Manpower** | Project - S Curve | Qty-Curve | Variation Curve

Plan & Actual by Week

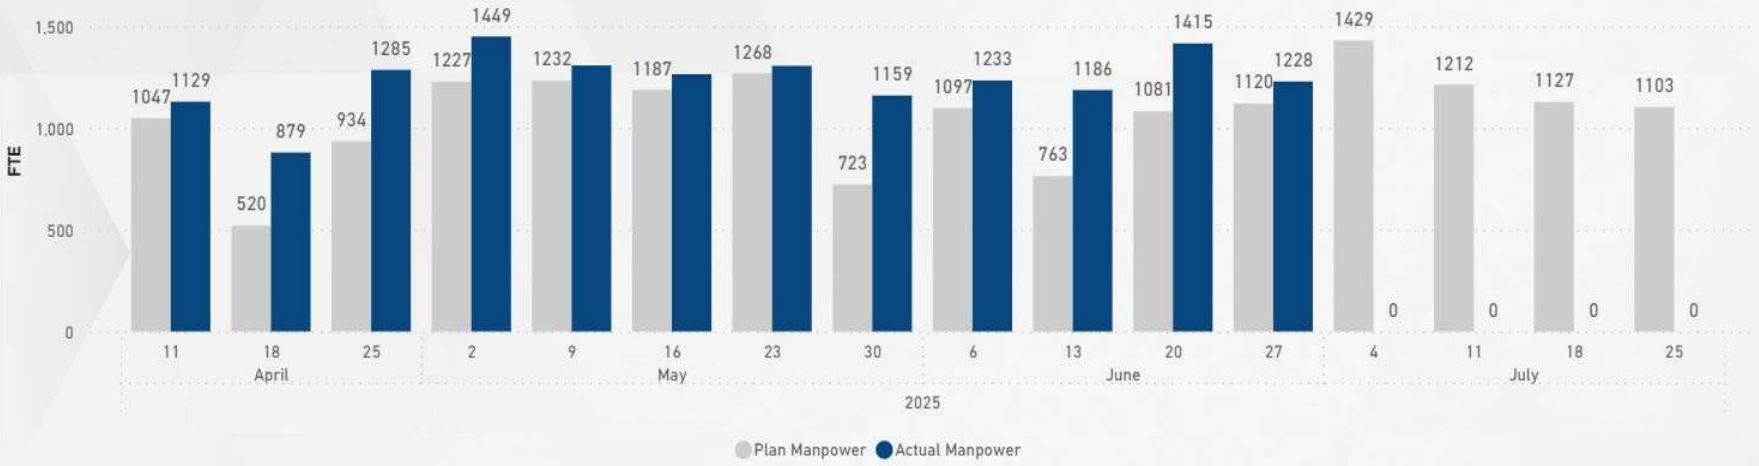

1228 ✓

Target: 1120 (+9.64%)

27-Jun-25

Contract

- ☐ K020 Structural Steel
- ☐ K030 Roofing and Cladding
- ☐ K031 Clean Rooms
- ☐ K032 Architecture - East
- ☐ K033 Architecture - West
- ☐ K045 HVAC East
- ☐ K046 HVAC West
- ☐ K050 Pipe Racks East
- ☐ K051 UG Process Drain
- ☐ K053 Fire Protection
- ☐ K055 Utility Piping East
- ☐ K056 Utility Piping West
- ☐ K057 Hygenic Piping
- ☐ K059 Passivation & Flushing
- ☐ K061 E&I - DSM4
- ☐ K062 E&I - West
- ☐ K063 E&I - Headblock
- ☐ K064 Electrical HV Contract
- ☐ K065 E&I - DSM5
- ☐ K070 Fire Alarm
- ☐ K071 BMS & EMS

Description	Contractor Name	Year	2025														
		Month	April			May					June				July		
			11	18	25	2	9	16	23	30	6	13	20	27	4	11	18
K020 Structural Steel	CSK	Plan Manpower	37	19	42	57	50	40	41	23	29	17	26	19	15	11	5
		Actual Manpower	31	20	37	36	27	17	16	15	15	15	0	▽ 0	0	0	0
K030 Roofing and Cladding	Kai Andersen	Plan Manpower	23	11	13	22	20	16	18	7	15	12	25	23	21	28	22
		Actual Manpower	23	14	34	36	29	25	28	8	27	17	34	▽ 16	0	0	0
K031 Clean Rooms	KCS	Plan Manpower	23	15	26	54	49	37	39	25	38	38	52	55	51	68	51
		Actual Manpower	32	13	18	58	48	45	30	27	37	37	35	▽ 38	0	0	0
K032 Architecture - East	Ardmac	Plan Manpower	145	70	115	160	208	181	186	89	141	69	98	102	130	112	93
		Actual Manpower	166	129	160	136	142	139	140	121	119	107	115	▽ 91	0	0	0
K033 Architecture - West	Jakon	Plan Manpower	8	4	5	4	7	8	8	3	5	5	8	10	15	18	15
		Actual Manpower	14	9	27	10	9	13	9	9	6	10	10	△ 10	0	0	0
K045 HVAC East	Dornan HVAC	Plan Manpower	41	16	36	44	61	56	62	34	60	34	54	59	78	74	57
		Actual Manpower	35	24	31	44	58	33	48	51	63	55	60	△ 65	0	0	0
K046 HVAC West	Priority Engineering	Plan Manpower	21	14	20	23	26	24	29	23	21	20	22	20	21	20	14
		Actual Manpower	19	9	17	30	27	22	15	21	30	36	28	▽ 13	0	0	0

Project Completion Timeline – Feb–Mar 2023

Key Contributions:

- Tracked completion status across 10+ systems
- Visualized weekly task completion and readiness
- Supported commissioning coordination

Tools & Techniques:

SQL, Power BI, Power Query, Gantt Chart Tools

Value Creation:

Improved cross-discipline coordination and milestone tracking

Project Completion Timeline – Feb–Mar 2023


Turnover Progress | Project System MC | System MC - PIPING | MC Skyline | QVD Rundown Curve | QVD Target Tracker

Di synth biotechnologies

QVD Status

27-04-2025 14-07-2025

Inc. Plan Inc. Actual Cum. Plan Cum. Actual



Path to WFI: All

Building: All


Contractor No.: All

Year	2025										
Month	May					June				July	
	2	9	16	23	30	6	13	20	27	4	11
Inc. Plan	126	590	245	509	503	682	1811	721	1961	1915	2120
Cum. Plan	2681	3271	3516	4025	4528	5210	7021	7742	9703	11618	13738
Inc. Actual	305	159	490	369	298	351	343	892	569	627	
Cum. Actual	4996	5155	5645	6014	6312	6663	7006	7898	8467	9094	9094

Walkdown 2 Status

11-04-2025 04-07-2025

Inc. Plan Inc. Actual Cum. Plan Cum. Actual



Path to WFI: All

Building: All


Contract: All

Year	2025														
Month	April			May					June					July	
	11	18	25	2	9	16	23	30	6	13	20	27		4	
Inc. Plan (BL 3.1)	20	55	23	26	56	141	148	140	91	89	46	60	74		
Cum. Plan (BL 3.1)	173	228	251	277	333	474	622	762	853	942	988	1048	1122		
Inc. Actual	5	6	13	22	7	43	16	35	23	8	41	29	28		
Cum. Actual	193	199	212	234	241	284	300	335	358	366	407	436	464		

Walkdown 3 Status

15-04-2025 14-07-2025

Inc. Plan Inc. Actual Cum. Plan Cum. Actual



Path to WFI: All

Building: All


Contract: All

Year	2025													
Month	April		May					June					July	
	18	25	2	9	16	23	30	6	13	20	27	4	11	
Inc. Plan (BL 3.1)	17	40	77	12	23	55	141	149	143	92	89	46	60	
Cum. Plan (BL 3.1)	121	161	238	250	273	328	469	618	761	853	942	988	1048	
Inc. Actual	3	16	32	27	14	6	8	11		17	4	72		
Cum. Actual	115	131	163	190	204	210	218	229	229	246	250	322	322	

MC Status

07-04-2025 30-07-2025

Inc. Plan Inc. Actual Cum. Plan Cum. Actual




MC Path to WFI: All

Building: All

Year	2025																	
Month	April			May					June					July				
	11	18	25	2	9	16	23	30	6	13	20	27	4	11	18	25		
Inc. Plan (BL 3.1)	1		4	4	3	8	4	4	5	20	28	60	37	31	47	47		
Cum. Plan (BL 3.1)	9	9	13	17	20	28	32	36	41	61	89	149	186	217	264	311		
Inc. Actual	3	2			1		2		13		1		7					
Cum. Actual	28	30	30	30	31	31	33	33	46	46	47	47	54	54				

Project Completion Timeline (Skyline)

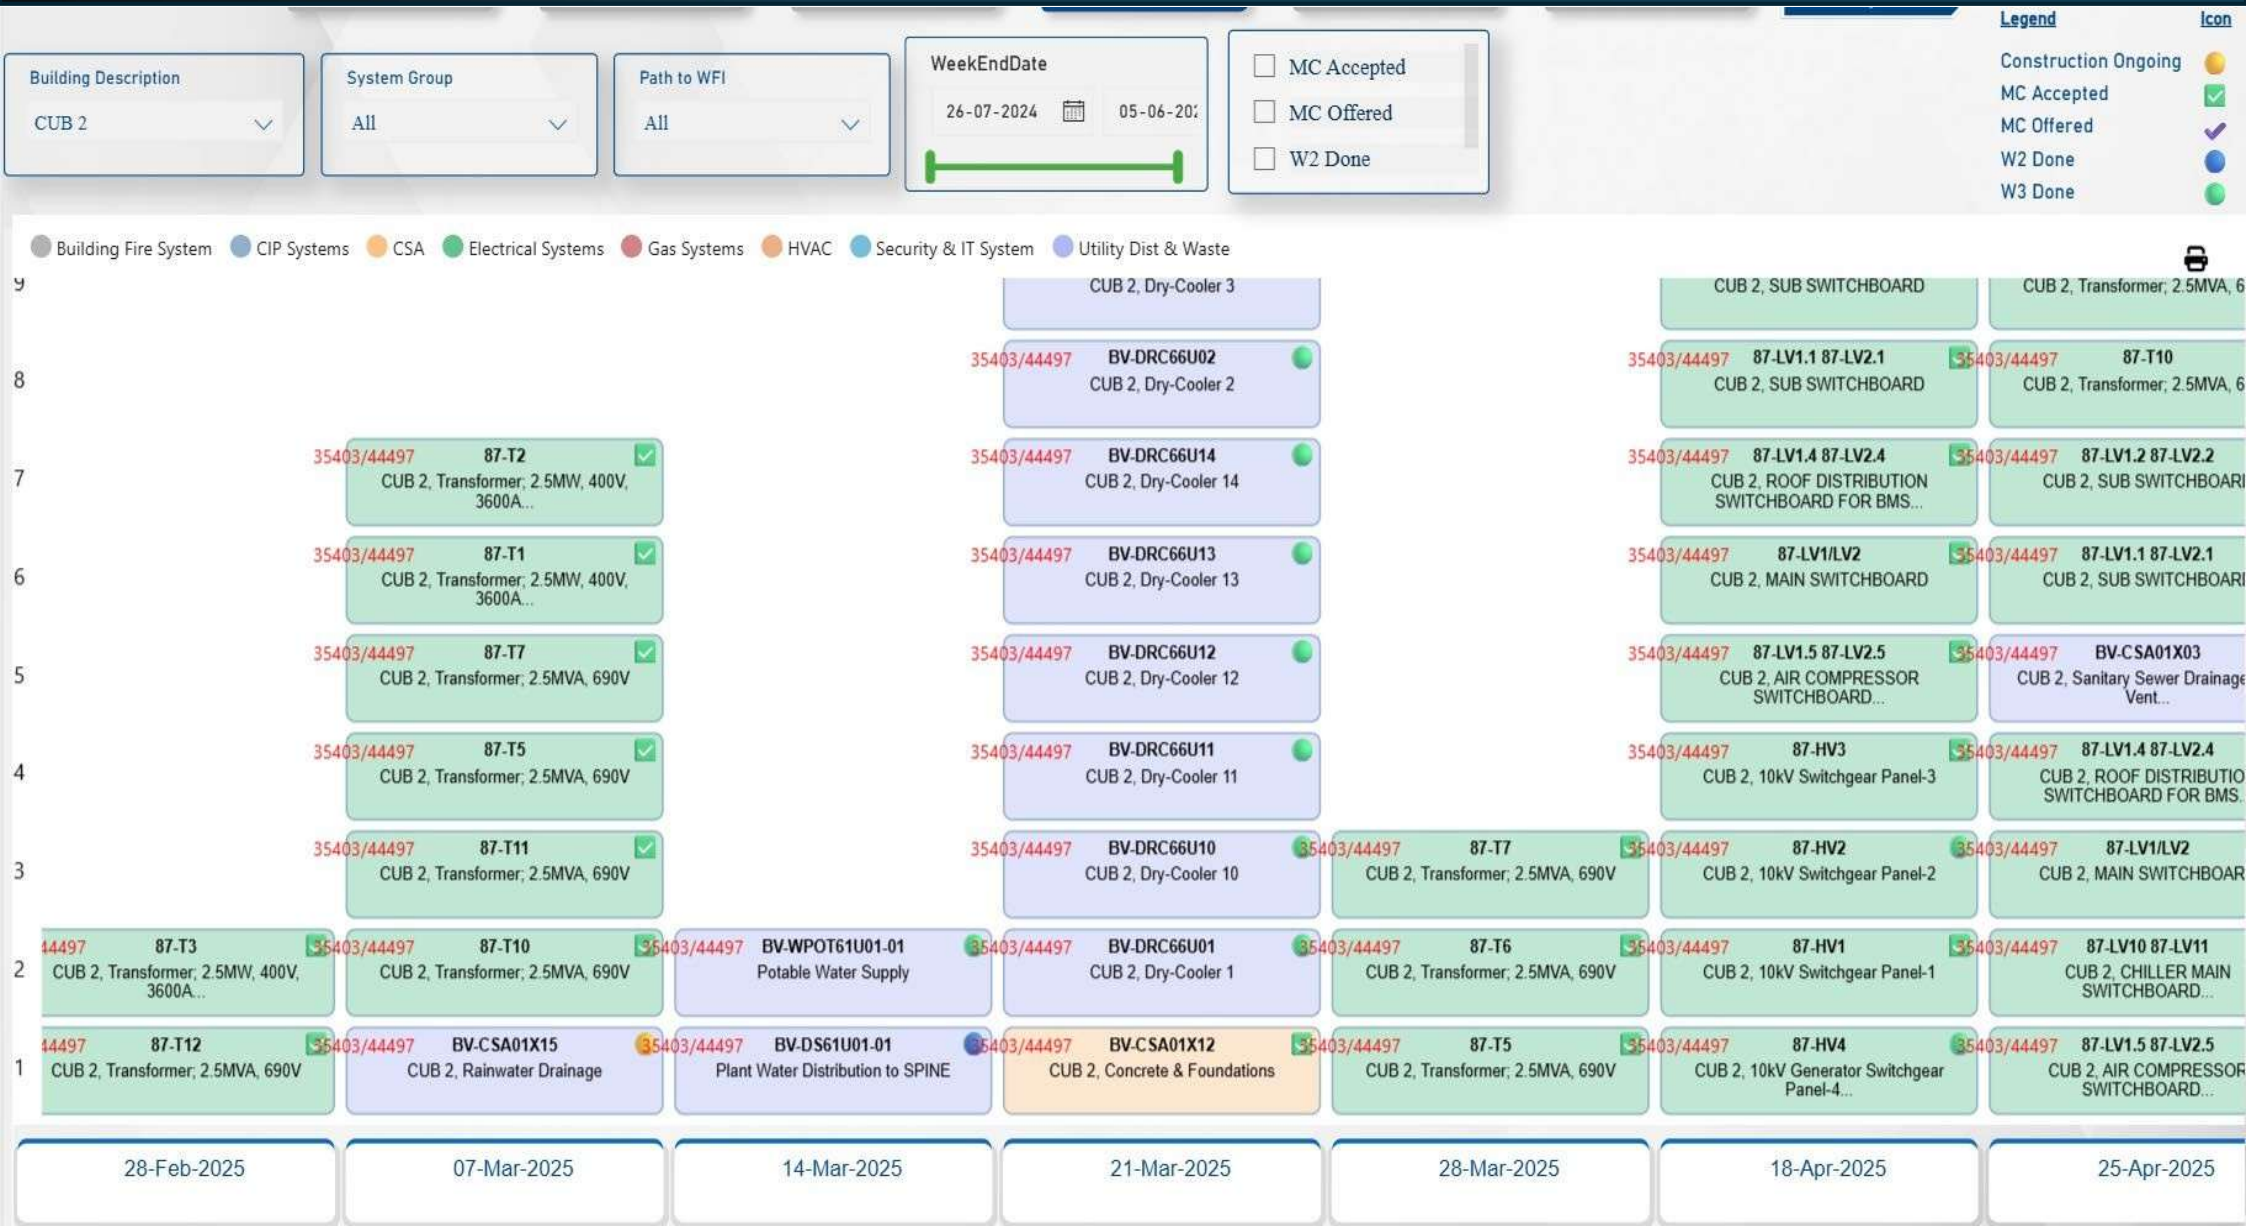

Schedule Deviation Dashboard

Key Contributions:

-Analyzed deviation rates across multiple area

-Built deviation summary tables and charts

-Tracked average deviation time by package

Tools & Techniques:

- Power BI, SQL, DAX, Schedule Deviation Analysis

Value Creation:

- Reduced reporting errors by 25% and improved schedule visibility

Schedule Deviation Dashboard

#Building

Select all	81	83	84	87	88

CWPs Schedule Deviation Rate



CWP Schedule Deviation Summary

Area	Early Start	Late Finish	On Schedule	Total
81 - HB	10	3	73	**86**
83 - DSM4	61	46	380	**487**
84 - DSM5	70	23	386	**479**
87 - CUB	35	22	164	**221**
88 - SPINE	16	4	35	**55**
Total	**192**	**98**	**1038**	**1328**


Overall

Count of Deviated IWPs



Average Deviation Time 4.05

Avg Delay (Days) per CWP

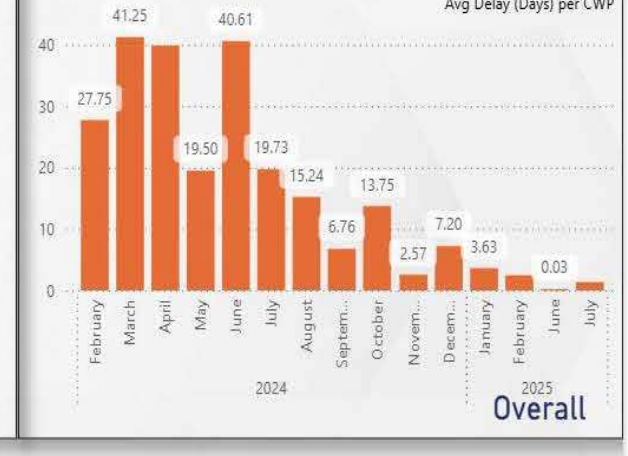

Area	Contractor	Contract	CWPNumber	CWPDescription	CWP QTY	First UOM	CWPPlanned Start	CWPPlanned Finish	IWPNumber	IWPDescription	IWPPurpose	IWPStatus	IWPKeyQty	UoM	IWPPlanned Start	IWPPlanned Finish	IWP Dura
83 - DSM4	Dornan	K045	83300101HFHV1HB	DSM4 - Heating, Ventilating, and Air Conditioning (HVAC) - Ground Floor - High Bay - Field Installation - HVAC - Sector 1 - High Bay	643.00	SM	07-Mar-22	23-Dec-26	83300101HFHV1HB-I001	Level 01 - Sector 1 / High Bay HVAC / DSM4 – Installation - First & Second fix of ductwork within Electrical closet 83-01230 -	HVAC Ducting Installation	Construction Complete	8	m^2	03-Jun-24	10-Jun-24	
83 - DSM4	Dornan	K045	83300101HFHV1HB	DSM4 - Heating, Ventilating, and Air Conditioning (HVAC) - Ground Floor - High Bay - Field Installation - HVAC - Sector 1 - High Bay	643.00	SM	07-Mar-22	23-Dec-26	83300101HFHV1HB-I002	Level 01 - Sector 1 / High Bay HVAC / DSM4 – Installation - First & Second fix of ductwork within Purification Rooms - 83-01620 + 83-01600	HVAC Ducting Installation	Closed Out	200	m^2	01-Jul-24	15-Jul-24	
83 - DSM4	Dornan	K045	83300101HFHV1HB	DSM4 - Heating, Ventilating, and Air Conditioning (HVAC) - Ground Floor - High Bay - Field Installation - HVAC - Sector 1 - High Bay	643.00	SM	07-Mar-22	23-Dec-26	83300101HFHV1HB-I003	Level 01 - Sector 1 / High Bay HVAC / DSM4 – Installation - First fix of ductwork in the Initial Purification Product Hold room 83-01625 - 83300101FHV1HB-I503	HVAC Ducting Installation	Construction Complete	55	m^2	08-Jul-24	29-Jul-24	
83 - DSM4	Dornan	K045	83300101HFHV1HB	DSM4 - Heating, Ventilating, and Air Conditioning (HVAC) - Ground Floor - High	643.00	SM	07-Mar-22	23-Dec-26	83300101HFHV1HB-I004	Level 01 - Sector 1 / High Bay HVAC / DSM4 – Installation -	HVAC Ducting	Draft Approved	50	m^2	09-Sep-24	07-Oct-24	

Gantt Chart Schedule Tracker

Key Contributions:

- Created Gantt chart for task timelines and durations
- Tracked progress % and milestone completion
- Used in weekly planning meetings


Tools & Techniques:

SQL, DAX, MS Project, Gantt Chart Design


Value Creation:

Improved task-level execution visibility and planning alignment


Gantt Chart Schedule Tracker

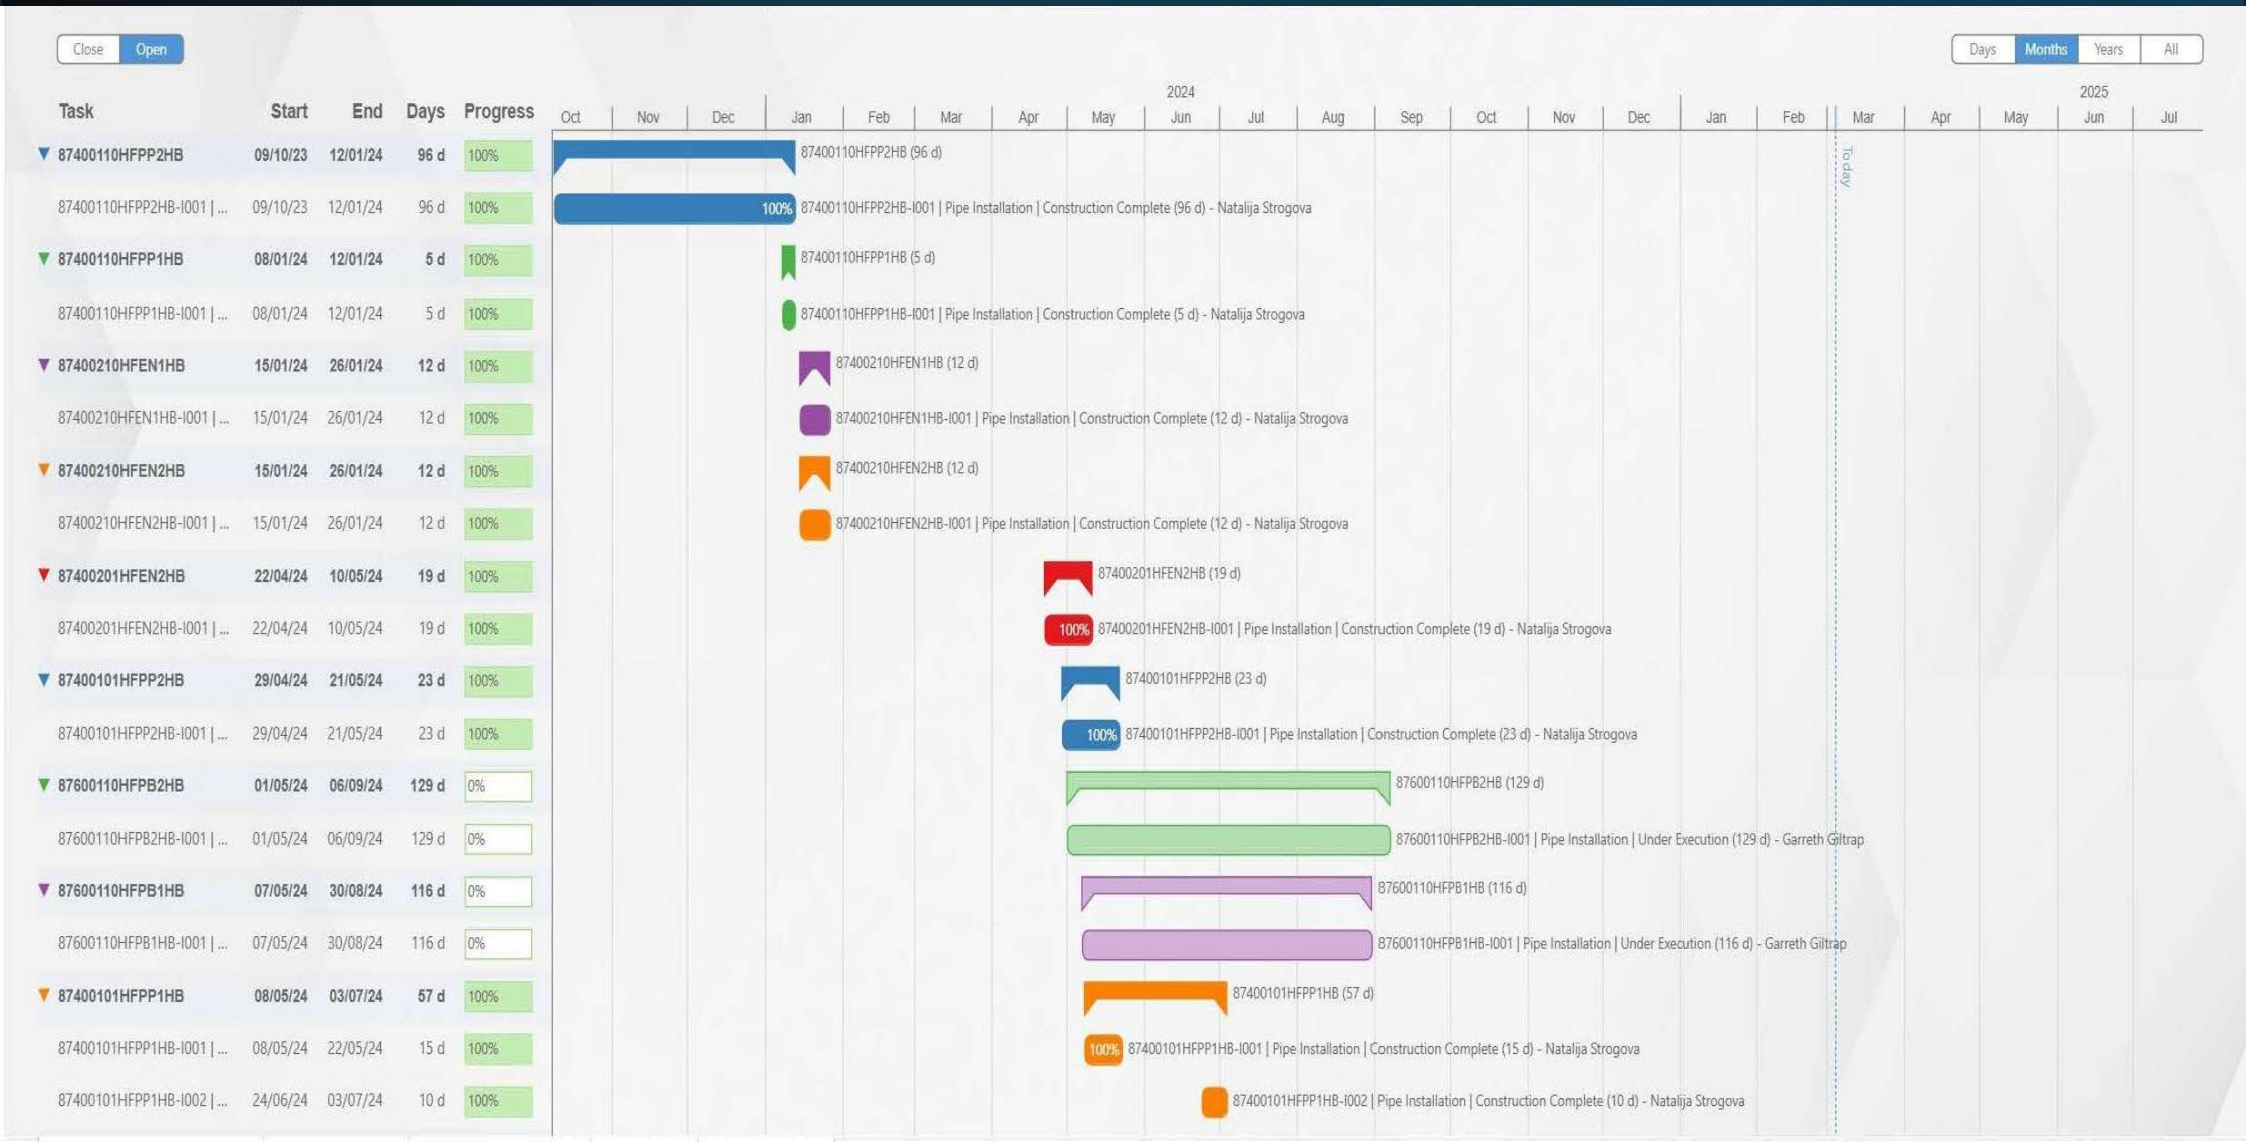

Gantt Chart Schedule Tracker

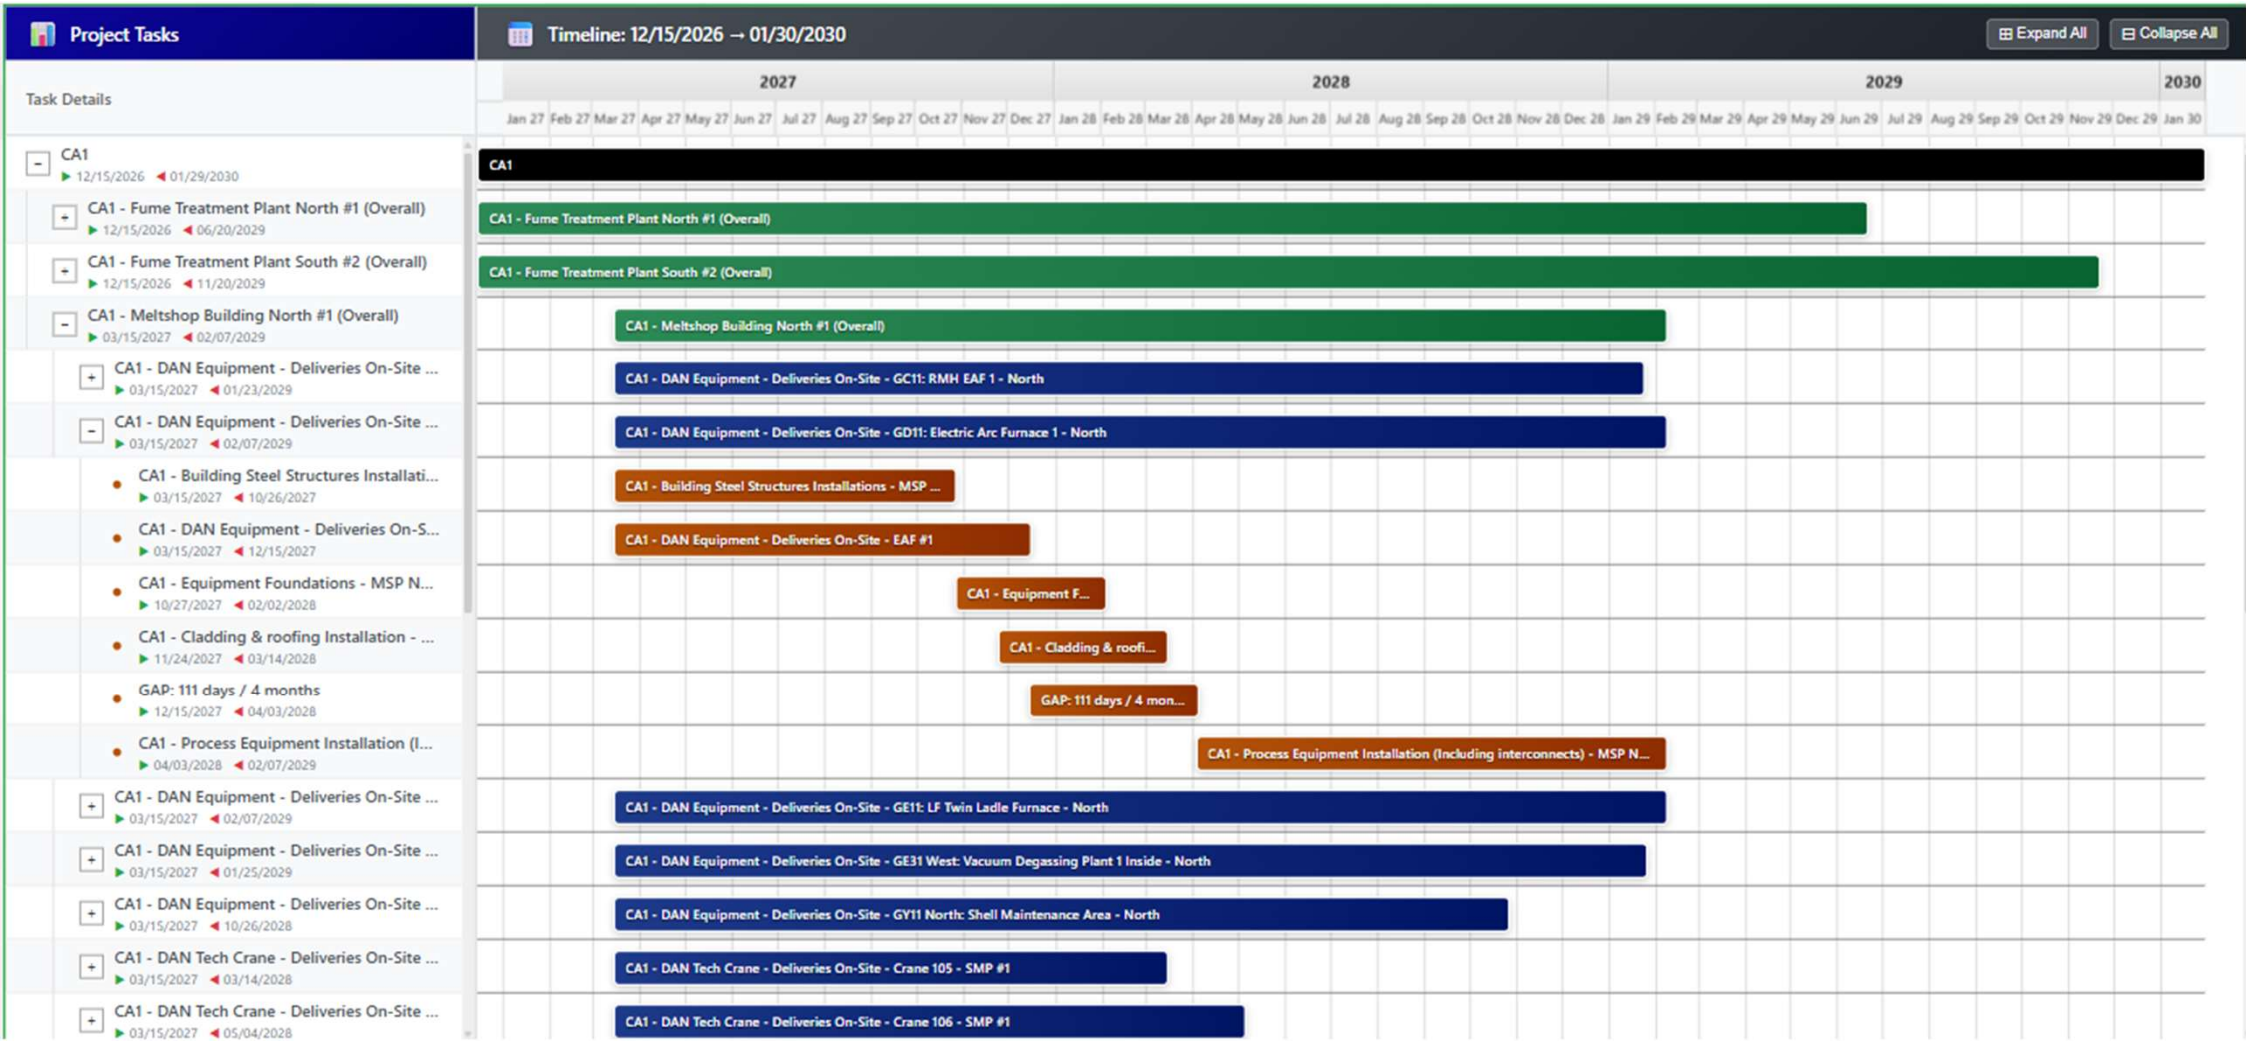

Geo-Map Progress & Alerts

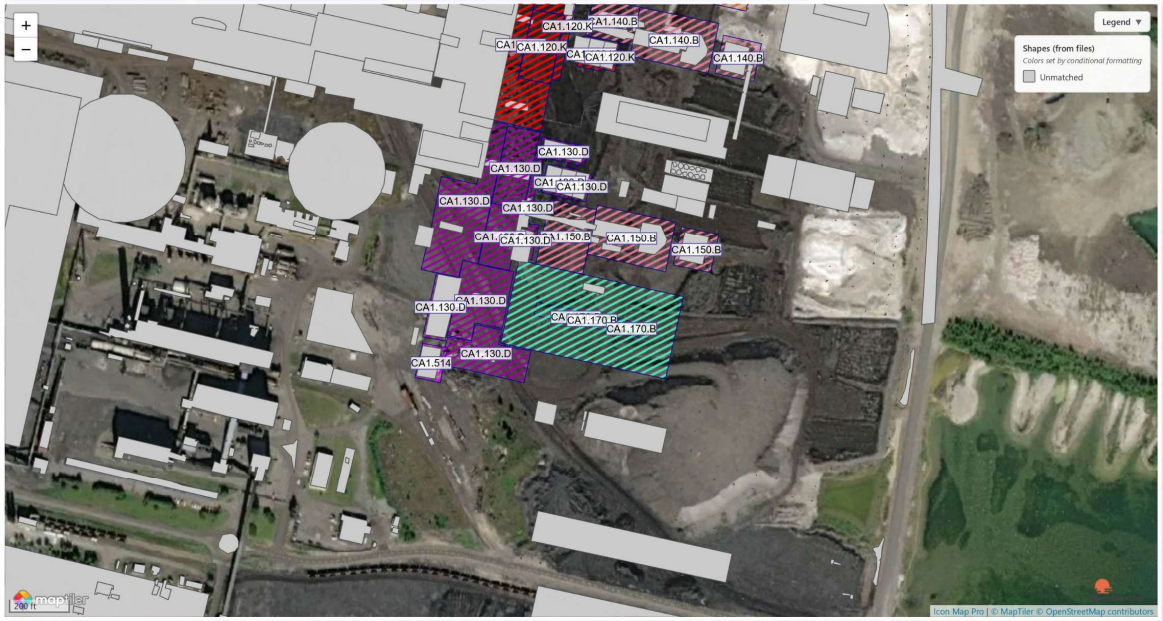

Today: 04-Nov 2026 | Current Week: 2026-W45 |
Week End: Fri, 6-Nov 2026

Look Ahead (6 Weeks) | Fri, 13-Nov 2026 → Fri, 18-Dec 2026

Unit	Sub Unit	Control Process	2026-W46	2026-W47	2026-W48	2026-W49	2026-W50	2026-W51
120. Meltsh...	CA1.1...	Building Foundations	156	156	156	156	156	94
	CA1.1...	Equipment Foundations	130	130	130	197	243	145
	CA1.1...	Piling	148	-	-	-	-	-
	CA1.1...	Piling	161	217	300	300	300	180
	CA1.1...	Piling	125	293	293	296	544	327
130. Meltsh...	CA1.1...	Deep Compaction	192	192	192	192	192	115
	CA1.1...	Piling	71	71	71	71	78	80
	CA1.1...	Piling	-	528	528	528	709	588
140. Fume T...	CA1.1...	Piling	-	-	-	141	267	196
	CA1.1...	Piling	425	607	790	158	-	-
150. Fume T...	CA1.1...	Deep Compaction	192	192	192	192	192	115
160. Endles...	CA1.1...	Building Foundations	144	144	144	144	144	86
		Deep Compaction	192	192	192	192	192	115
	CA1.1...	Equipment Foundations	-	79	131	131	131	79
170. Endles...	CA1.1...	Deep Compaction	9	9	9	9	9	5
		Piling	429	1,070	1,070	1,530	1,616	1,192
	CA1.1...	Equipment Foundations	100	100	100	100	100	60
513. MSP N...	CA1.5...	Building Foundations	29	29	29	42	54	33



